

N00102.AR.003150
NSY PORTSMOUTH
5090.3a

FINAL SITE MANAGEMENT PLAN FISCAL YEAR 2015 NSY PORTSMOUTH ME
01/01/2015
RESOLUTION CONSULTANTS

SITE MANAGEMENT PLAN FISCAL YEAR 2015

NAVAL SHIPYARD PORTSMOUTH
KITTERY, MAINE

Final

Prepared for:



Department of the Navy
Naval Facilities Engineering Command, Mid-Atlantic
9742 Maryland Avenue
Norfolk, VA 23511-3095

Comprehensive Long-Term Environmental Action Navy
Contract Number N62470-11-D-8013

CTO WE05-02

Prepared by:



Resolution Consultants
A Joint Venture of AECOM & EnSafe
1500 Wells Fargo Building
440 Monticello Avenue
Norfolk, VA 23510

January 2015

Table of Contents

ACRONYMS AND ABBREVIATIONS.....	iii
1.0 INTRODUCTION.....	1
2.0 SETTING AND ENVIRONMENTAL HISTORY.....	2
2.1 Facility Mission and History.....	2
2.2 Understanding of the Environmental Conditions	3
2.3 Community Participation.....	5
3.0 DESCRIPTION OF ENVIRONMENTAL SITES	6
3.1 Operable Unit 1 (OU1)	7
3.2 Operable Unit 2 (OU2)	10
3.3 Operable Unit 3 (OU3)	15
3.4 Operable Unit 4 (OU4)	19
3.5 Operable Unit 7 (OU7)	25
3.6 Operable Unit 8 (OU8)	27
3.7 Operable Unit 9 (OU9)	30
3.8 Site Screening Area	33
4.0 SITE RANKING.....	37
5.0 SCHEDULES	38
6.0 LAND USE PLANNING	39
7.0 REFERENCES	40

TABLES

Table 1	Major Phases of the CERCLA Process
Table 2	Summary of Environmental Restoration Program Sites
Table 3	Summary of Sites Removed from the Environmental Restoration Program
Table 4	Summary of Relative Risk Ranking and Remediation Activities Performed

FIGURES

Figure 1	Site Location Map
Figure 2	Portsmouth Naval Shipyard Facility Plan View Map
Figure 3	Portsmouth Naval Shipyard Facility Aerial View Map
Figure 4	Portsmouth Naval Shipyard Facility Bird's Eye View
Figure 5	Portsmouth Naval Shipyard Interim Offshore Monitoring Station Locations

ATTACHMENTS

Attachment A	List of ERP Documents for Portsmouth Naval Shipyard
Attachment B	Schedules
Attachment C	June 2014 Schedule Revisions For FY15 Amended Site Management Plan

ACRONYMS AND ABBREVIATIONS

AOC	Area of Concern
ARF	Administrative Record File
bgs	Below ground surface
CDC	Child Development Center
CERCLA	Comprehensive Environmental Response, Compensation and Liability Act
CHF	Contaminant Hazard Factor
CIA	Controlled Industrial Area
CIP	Community Involvement Plan
CMI	Corrective Measures Implementation
CMS	Corrective Measures Study
CNO	Chief of Naval Operations
COPC	Chemical of Potential Concern
DoD	Department of Defense
DRMO	Defense Reutilization and Marketing Office
EE/CA	Engineering Evaluation/Cost Analysis
EERA	Estuarine Ecological Risk Assessment
ERP	Environmental Restoration Program
ESD	Explanation of Significant Difference
FCS	Final Confirmation Study
FFA	Federal Facilities Agreement
FS	Feasibility Study
FY	Fiscal Year
HHRA	Human Health Risk Assessment
HRS	Hazard Ranking System
HSWA	Hazard and Solid Waste Amendments (of 1984)
IAG	Interagency Agreement
IAS	Initial Assessment Study
IRG	Interim Remediation Goal
JILF	Jamaica Island Landfill
LUCs	Land Use Controls

LUCRD	Land Use Control Remedial Design
MB	Mercury Burial
MEDEP	Maine Department of Environmental Protection
mg/kg	Milligram per kilogram
MIDLANT	Mid-Atlantic
MILCON	military construction
MPF	Migration Pathway Factor
NACIP	Navy Assessment and Control of Installation Pollutants
NAVFAC	Navy Facilities Engineering Command
NFA	No Further Action
NPL	National Priorities List
OM&M	Operation, maintenance, and monitoring
OU	Operable Unit
PA	Preliminary Assessment
PAH	Polycyclic aromatic hydrocarbon
PCB	Polychlorinated biphenyl
PNS	Portsmouth Naval Shipyard
PP	Proposed Plan
PRAP	Proposed Remedial Action Plan
PRG	Preliminary Remediation Goal
RA	Remedial Action
RAB	Restoration Advisory Board
RACR	Remedial Action Completion Report
RC	Response Complete
RCRA	Resource Conservation and Recovery Act
RD	Remedial Design
RF	Receptor Factor
RFA	RCRA Facility Assessment
RFI	RCRA Facility Investigation
RI	Remedial Investigation
RIP	Remedy in Place
ROD	Record of Decision
SI	Site Investigation

SMP	Site Management Plan
SSA	Site Screening Area
SSI	Site Screening Investigation
SSP	Site Screening Process
SWMU	Solid Waste Management Unit
SVOC	Semi-volatile organic compound
TCLP	Toxicity Characteristic Leaching Procedure
USEPA	United States Environmental Protection Agency
VOC	Volatile organic compound

1.0 INTRODUCTION

This document is an Amended Site Management Plan (SMP) for Fiscal Year (FY) 2015 for the Portsmouth Naval Shipyard (PNS) in Kittery, Maine. This report was prepared for the Naval Facilities Engineering Command, Mid-Atlantic (NAVFAC MIDLANT), by Resolution Consultants under Contract Number N62470-11-D-8013 (Contract Task Order CTO WE05-02). The purpose of the SMP is to provide a management tool to be used by the Navy, United States Environmental Protection Agency (USEPA), and Maine Department of Environmental Protection (MEDEP) in planning, reviewing, and setting priorities for all environmental investigative and remedial response activities to be conducted at the facility under the Navy Environmental Restoration Program (ERP). The primary components of the SMP include:

- Summary of site location, mission, history, and environmental activities
- Overview of ERP activities since the previous SMP
- Changes in site conditions or risk exposures since the previous SMP
- Estimated schedule of upcoming activities and completion

The SMP is updated annually to revise schedules, deadlines, and milestones for the next FY based on funding, changes in scope of investigation and remediation activities, changes in site conditions, and/or other unanticipated events. This annual amendment to the SMP meets the requirements of Section XI (Subsections 11.4 and 11.5) of the Federal Facilities Agreement (FFA) for Portsmouth Naval Shipyard.

2.0 SETTING AND ENVIRONMENTAL HISTORY

The following section summarizes the location, mission, history, and environmental activities at PNS. Figure 1 illustrates the location of the Installation. Figures 2 and 3 present plan and aerial views of the shipyard delineating the Operable Units (OUs) and active ERP Sites. Figure 4 presents a bird's eye view of PNS.

2.1 Facility Mission and History

PNS is a military facility with restricted access on Seavey Island located in the Piscataqua River at the mouth of Portsmouth Harbor between Kittery, ME and Portsmouth, NH (Figure 1). The primary mission of PNS is the conversion, overhaul, and repair of submarines for the Navy. Shipbuilding in Portsmouth Harbor dates back to 1690, and PNS was established as a government facility in 1800. The first government-built submarine was designed and constructed at PNS during World War I, and a large number of submarines have been designed, constructed, and repaired at this facility since 1917. Present military activities are concentrated in the western portion of the facility in the Controlled Industrial Area (CIA). This area includes dry docks, submarine berths, and numerous buildings that house trade shops related to maintenance activities. Access to the area is tightly controlled and limited to individuals having appropriate clearances. Uses of other portions of PNS include administration offices, officers' residences, equipment storage, parking, and recreational facilities.

Areas within PNS are included on the National Register of Historic Places including the area between the two bridges connecting PNS to Kittery, Maine, the majority of the CIA, and the Portsmouth Naval Hospital and Portsmouth Naval Prison Historic Districts.

Water for operations and drinking at the Shipyard are supplied by the Kittery Water District. Kittery's water supply originates from surface reservoirs located in the vicinity of York, Maine. Groundwater at PNS is not used for drinking, irrigation, industrial processes, fire fighting, or any other purposes.

The Navy ERP Program at the Shipyard has been dedicated to environmental stewardship in performing activities to assess and clean up hazardous substances. In 2012, PNS was honored with both the Secretary of the Navy and Chief of Naval Operations (CNO) awards for the Environmental Restoration (Large Installation category), the Navy's top environmental award for its environmental restoration efforts during FY 2011 at large installations. In 2013, PNS was again awarded the CNO award for Environmental Restoration (Large Installation category) for FY 2012.


2.2 Understanding of the Environmental Conditions

Shipbuilding and submarine repair work at PNS resulted in hazardous substances being released into the soil, groundwater, surface water, and sediment on and around Seavey Island. Investigation and remediation activities have been performed under the ERP to reduce potential risks to human health and the environment by identifying, assessing, characterizing, and cleaning up or controlling releases of hazardous substances. Investigations of hazardous substance releases at PNS began in 1983 when the Navy completed an Initial Assessment Study (IAS) [Weston, June 1983] that identified and assessed sites posing a potential threat to human health and the environment. The final phase of this study was completed in 1986 with the issuance of a Final Confirmation Study (FCS), [LEA, June 1986], which evaluated the sites identified in the IAS to confirm the presence of contamination. Investigations of PNS hazardous waste sites prior to 1986 were conducted under the Navy Assessment and Control of Installation Pollutants (NACIP) Program, and since 1986, investigations at PNS have been conducted under the ERP.

USEPA became involved with PNS in 1985 when the agency requested information on PNS's hazardous wastes and conducted a visual site inspection under Resource Conservation and Recovery Act (RCRA) authority. MEDEP has also provided oversight of investigation and remediation at PNS since 1988. USEPA issued a Corrective Action Permit in March 1989 under the RCRA Hazardous and Solid Waste Amendments (HSWA) of 1984 [USEPA, March 1989] requiring PNS to investigate 13 Solid Waste Management Units (SWMUs) and take appropriate corrective action. Most environmental activities at PNS were initiated under RCRA in accordance with the HSWA permit. Following inclusion on the NPL in May 1994, environmental activities at the Shipyard are now governed by the Comprehensive Environmental Response, Compensation and Liability Act (CERCLA) as described in the FFA.

In 1993, the PNS sites were evaluated by USEPA under CERCLA's Hazard Ranking System (HRS) to determine the relative threats posed to the public health and environment by sites contaminated with hazardous substances [TRC, May 1993]. The HRS scores sites based on the potential for hazardous substances to spread from the site through air, surface water, and groundwater and consider additional ranking factors including population, waste characterization, and potential damage to natural resources. Based on the HRS evaluation, PNS was proposed for inclusion on the USEPA's National Priorities List (NPL) in June 1993, and was included on the NPL on May 31, 1994. After this date, all subsequent environmental investigations and cleanup activities have been conducted under the authority of CERCLA. CERCLA includes a process with sequential phases to evaluate the nature and extent of contamination at a site; determine the need for a remedy; and if necessary identify, develop, and implement appropriate remedial actions in order to protect human

health and the environment. The major phases of the CERCLA process, for which the ERP parallels, are shown in the graphic below and are described in greater detail in Table 1.

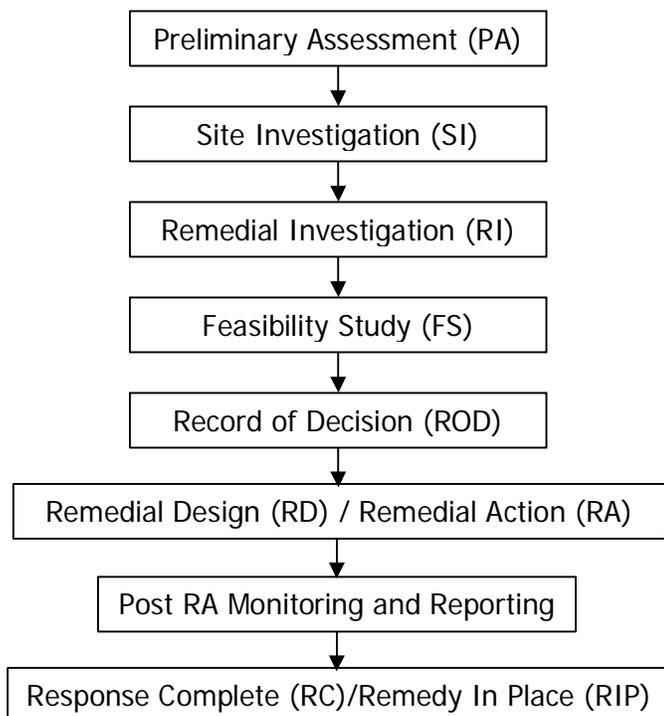

Not all phases of the CERCLA process are required for every site.

The onshore and offshore components of work required by the HSWA Permit was directed to be separated by USEPA in 1994 such that activities within the onshore portion of the facility would not be further delayed by the more complex offshore investigations. However, potential impacts from onshore sites to offshore areas were evaluated as part of the onshore studies, as discussed further in the site- or OU-specific discussions in Section 3.0.

The FFA for PNS was signed by the Navy and USEPA in September 1999, became effective February 2000, and superseded the HSWA Permit. The State of Maine elected not to be a party to the FFA. However, the state is afforded a participatory role in the site remediation process by virtue of CERCLA. The FFA establishes the roles and responsibilities of the Navy, USEPA, and MEDEP under CERCLA, establishes deadlines/schedules, outlines work to be performed, and provides a dispute resolution process for primary documents. This annual amendment to the SMP meets one of the requirements of the FFA (Section 11.4).

2.3 Community Participation

PNS has established a Restoration Advisory Board (RAB) comprised of members of the community, local environment group members, and federal and state officials, who meet as needed between September and June to keep the community and stakeholders informed on environmental issues at PNS. An index of the documents prepared for the program is maintained in the administrative record for review by the public at repositories at the Portsmouth Public Library in Portsmouth, New Hampshire and the Rice Public Library in Kittery, Maine. Additionally, the Navy hosts a public website for the Shipyard that includes site description and background information, Community Outreach information, and access to the Administrative Record File (ARF), which allows the community to download any of the final pre-decision documents for the Shipyard. The weblink to the public website is <http://go.usa.gov/DyRH>.

All documents from the administrative record are available through the Public Affairs Officer for PNS at:

Public Affairs Office, Code 100PAO
Portsmouth Naval Shipyard
Portsmouth, NH 03804-5000
Phone: (207) 438-1140
PORT_PTNH_ASK_PAO@navy.mil

A Community Involvement Plan (CIP) was prepared and finalized in June 2012. The 2012 CIP was an update of the previous CIP that was updated in 1996 (Brown and Root, 1996).

3.0 DESCRIPTION OF ENVIRONMENTAL SITES

There are currently 10 on-shore sites that are undergoing various stages of environmental restoration. The initial investigations of PNS identified 28 potential sites (referred to as SWMUs at that time under RCRA) located onshore and offshore of PNS. After the 28 potential sites were examined in detail, 15 were eliminated from further investigation, leaving 13 sites that required additional investigation and appropriate corrective action [Kearney & Baker/TSA, July 1986]. These 13 sites were listed in the HSWA Permit. Following the HSWA, four were identified as No Further Action (NFA) sites, a portion of Site 6 was separated and given a separate number (Site 29), and four sites were newly identified. The 1999 FFA included 14 sites and the offshore area, and since that time four additional sites and the Jamaica Island Landfill (JILF) Impact Area (within Site 8) have been removed from the ERP, including Site 30 through a No Further Action Decision Document in 2014. The remaining sites (referred to as the ERP sites) are under various stages of investigation/remediation and listed below.

Current PNS ERP Sites	PNS Sites Removed from the ERP
5, 6, 8, 9, 10, 11, 29, 31, 32, 34 Offshore AOCs	1, 2, 3, 4, 7, 12, 13, 14, 15, 16, 17, 18, 19, 20, 21, 22, 23, 24, 25, 26, 27, 28, 30, JILF Impact Area

The Navy organized the ERP sites into Operable Units (OUs) based on similar kinds of contamination and geographic proximity as an alternative to addressing all of the PNS sites as one large study area and cleanup action. The sites listed in the FFA were grouped into five OUs (OU1 through OU5). OU6 was identified in 2000 to address management of migration from the JILF; however, OU6 was recombined with OU3 through an Explanation of Significant Difference (ESD) for the OU3 ROD signed in October 2005 with management of migration of groundwater from the JILF addressed as part of the OU3 remedy. Further investigations resulted in designation of OU7, OU8, and OU9. In addition, OU5 was removed from the CERCLA list in 2001.

The locations of the OUs and ERP sites under investigation or remedial action are shown on Figures 2 and 3, and a summary of the status of active sites is provided in Table 2. A summary of the sites removed from the ERP is provided in Table 3. Additional information on site- or OU-specific investigations is provided in the discussion related to the specific OU or site screening area.

3.1 Operable Unit 1 (OU1)

Site Description

OU1 consists of

- Site 10 – Former Battery Acid Tank No. 24

Site 10 occupies a small peninsula located in the CIA near the southern shore of PNS (Figure 2), and is located within an area of current and historical industrial activities. Site 10 is located on fill material that was placed prior to the 1920s and includes Building 238 that was built in 1955 and was used for battery recharging operations that previously resulted in releases of contaminated wastewater. Currently, Building 238 is primarily used for office space. The soils within Site 10 are currently covered by Building 238 and asphalt. A crawl space with an earthen floor exists beneath a portion of Building 238 and the loading dock. The ground elevation of the earthen floor is approximately 5 to 6 feet below the ground elevation outside the building and loading dock.

Site 10 is bounded by buildings to the west and north and by the Piscataqua River on the east, south, and southwest. The Site 10 shoreline along the Piscataqua River from the west to the southeast is bounded by a quay wall of granite blocks. Barges are commonly docked at these berths located south and east of Building 238 (Berths 4 and 5).

The offshore area of Site 10 is part of the Dry Dock Area of Concern (AOC) which was investigated separately as part of the Estuarine Ecological Risk Assessment (EERA) [NCCOSC, May 2000; Johnston, et. al., December 1994]. Sampling locations within monitoring station MS-12 in the Interim Offshore Monitoring Program are located adjacent to OU1 and includes a depositional area west of Site 10 and south of Building 178. The offshore area is further discussed as part of OU4 in Section 3.4.

Nature and Extent of Potential Contamination

Large lead-acid storage batteries were drained inside Building 238 as part of the lead-acid recharging operations, and prior to 1974 the waste acids drained directly to the offshore through an industrial waste outfall (Site 5) [TtNUS, June 2006a; Weston, June 1983]. In 1974, waste acids were directed into a lead-acid drain pipeline to an underground storage tank. The drain line exited the building in the crawl space and then dropped vertically into the earthen floor of the crawl space. The acidic discharge flowed through the drain line through the floor of the building to a steel underground storage tank (Battery Acid Tank No. 24) of 9,680-gallon capacity. Use of the

pipng and tank was discontinued in 1984 when a leak was discovered in the tank. Tank closure was conducted in 1986, when the tank and surrounding contaminated soil were removed [TtNUS, June 2006a]. Testing of the soil during tank excavation indicated no exceedances of hazardous waste criteria.

Numerous soil and groundwater investigations were completed at Site 10 after the tank removal, between 1991 and 2006 [McLaren/Hart, July 1992; TtNUS, March 2000; TtNUS, March 2003; TtNUS, June 2006a]. The RI Report, completed in 2007, indicated that lead was the primary chemical of concern in soil in the area of the tank leak and soil in the crawl space by the drain line [TtNUS, July 2007]. Groundwater sampling results did not indicate that groundwater was a medium of concern for human health exposure or migration of groundwater for offshore impact (site groundwater concentrations were less than action levels).

The investigations showed fill material at the site was rocky and ranged in thickness from 10 feet to 40 feet, and was generally thickest nearer to the shoreline. Gravel, bricks, and other building materials were also found in the fill material. Groundwater at the site is tidally influenced and is saline or brackish. Past release(s) from site operations to the offshore area are being addressed as part of MS-12 within OU4. A list of important Site 10 historical events and environmental investigations with relevant dates is shown below.

Event	Date
Filling of area was conducted and area apparently used for berthing and/or launching boats	Before 1826 to 1860s and 1900s to 1915
Other industrial uses of area	1910s to 1920s
Building 238 built and lead-acid battery recharging operations began within the building	1955
Lead-battery acid wastes discharged directly to the river (through an industrial waste outfall that is part of Site 5)	1955 to 1974
Lead-battery acid wastes discharged to underground storage tank (Battery Acid Tank No. 24) south of Building 238	1974 to 1984
Leak in underground tank discovered and use of tank discontinued	1984
Tank closure conducted with underground tank and surrounding contaminated soil removed	1986
Sampling of soil and groundwater to determine nature and extent of contamination	1991, 1998, 2001, and 2006
Remedial Action	October 2011 to March 2012
LUC inspections	June 2013, May 2014

CERCLA Remedial Summary

During the development of the RI/FS several human health risks were identified that required remedial action, primarily associated with lead in surface and subsurface soils. In response to these risks, the selected remedy for OU1 in the ROD included excavation and off-yard disposal of contaminated soil with lead concentrations greater than acceptable levels for construction workers, recreational users, and occupational workers from around the drain lines within the crawl space under Building 238, as well as implementation of Land Use Controls (LUCs) to prevent future residential site use of the site [Navy, September 2010]. The Remedial Action at OU1 commenced in October 2011 and was completed in March 2012. Major reports prepared for OU1 under CERCLA are presented below.

Document	Author/Date	Administrative Record Number
Final OU1 RI Report	TtNUS, July 2007	001606
Final OU1 FS Report	TtNUS, June 2010	001754
Final OU1 PRAP	Navy, June 2010	001759
Final OU1 ROD	Navy, September 2010	002495
Final OU1 Remedial Action Work Plan	Shaw, October 2011	002627
Final OU1 LUCRD	Tetra Tech, January 2012	002643
Final Sampling and Analysis Plan for Post Remediation Groundwater	Tetra Tech, January 2012	002648
Final Round 1 Package for Post Remediation Groundwater Monitoring	Tetra Tech, August 2012	002764
Final Post-Remediation Groundwater Monitoring Report	Tetra Tech, July 2013	002864
Final Construction Completion Report	CB&I, September 2013	002945
Draft LUCRD Revision	Tetra Tech, June 2014	Draft Document
Draft Remedial Action Completion Report	Tetra Tech, June 2014	Draft Document

Activities Completed in FY 2014

The final Post-Remediation Groundwater Monitoring Report was submitted in July 2013 summarizing groundwater sampling conducted in February and November 2012 that concluded that all lead concentrations were less than Project Action Levels. The final Construction Completion Report was submitted in September 2013. LUC inspections that are part of the remedy commenced in June 2013 and were performed in May 2014. The draft Remedial Action Completion Report (RACR) was prepared and submitted in June 2014. A draft LUCRD Revision was submitted in June 2014.

CERCLA Path Forward

The CERCLA path forward for OU1 is as follows:

- Near Term Milestones
 - LUC Inspection
 - Remedial Action Completion Report (RACR)
- Out Year Milestones
 - LUC Inspections
 - Five-year reviews

The schedule for upcoming activities and milestones for OU1 is included in Attachment B.

3.2 Operable Unit 2 (OU2)

Site Description

OU2 consists of:

- Site 6 – DRMO Storage Yard, including the DRMO Impact Area
- Site 29 – Former Teepee Incinerator Site

OU2 is located in the south-central portion of PNS (Figure 2) along the Piscataqua River. The OU2 shoreline is steeply sloped and has shoreline erosion controls (riprap and a seawall) placed along portions of the shoreline to provide erosion protection. The OU2 shoreline is difficult and dangerous to access because of strong river currents and the steep embankment from the site to the river. Since the area was filled, the area within Sites 6 and 29 have been used as industrial and commercial areas. The DRMO Impact Area includes military residences. Within Site 6 the Defense Reutilization and Marketing Office (DRMO) was responsible for the reuse, transfer, donation, sale, or disposal of excess and surplus Department of Defense (DoD) property in New England. Until operations moved out in 2010, DRMO operations were conducted in the paved portion of the fenced area. There are no permanent buildings located at the DRMO (Site 6). An area that was capped in 1993 is covered with grass and barricaded from use for any activities. At Site 29, Building 298 is used for office space and Building 310 is the hose handling facility. There are no longer any hazardous waste-related activities at OU2, and hazardous chemicals are not used as part of any of the current operations.

There is a small intertidal sediment area adjacent to OU2 to the east, which is part of the DRMO Storage Yard AOC investigated as part of the EERA. A sampling location within monitoring station MS-11 in the Interim Offshore Monitoring Program is located in a depositional area east of the seawall at Site 29 [TtNUS, November 2010]. The offshore area is discussed as part of OU4 in Section 3.4.

Nature and Extent of Potential Contamination

The area around Site 6 was used for DRMO operations starting in approximately 1920 and has included storage of lead- and nickel-cadmium battery elements, motors, typewriters, paper products, and scrap metal. Historically, DRMO operations primarily occurred in the current fenced area of the DRMO, but operations also may have occurred in areas directly adjacent to the DRMO. The major hazardous materials of concern were the battery cells and plates that were stockpiled on uncovered pallets. Open storage of batteries and other materials that could cause contaminants to be leached or otherwise released by pathways such as infiltration or runoff were terminated in approximately 1983.

The main activities that occurred in the Site 29 area included open burning, waste disposal, and industrial incineration. A portion of Site 29, referred to as the Waste Disposal Area (WDA), was apparently filled with paper, wood, rubbish, and ash reportedly from open burning of trash conducted from approximately 1918 until 1965. A teepee incinerator (former Building 290) operated from 1965 to 1975 for disposal of wood, paper, rubbish, and occasional burning of cans of paint and solvents, and ash from the teepee incinerator was also disposed of in the WDA until 1971. Materials identified in soil borings located in the WDA are generally consistent with the background information and include ash, cinders, wire, glass, wood, and metal pieces. Asbestos was also found during the excavation of the Building 310 foundation, which is located over the WDA. Building 298 was built in 1975 and was used as an industrial waste treatment facility until the 1980s. Spill prevention and control methods were in place during operation of the facility, and there were no reported releases impacting soil or water outside the building.

Initial environmental sampling at OU2 began in 1984. Investigations have shown that Site 6 and much of Site 29 (in the area filled in the early 1900s as part of Henderson's Point excavation) consists of angular rock fragments overlain by general fill material composed of sand and gravel with minor amounts of wood and metal debris and cinders. Remaining filled areas of OU2 consist of sand, gravel, and silt overlying waste fill that includes cinders, ash, plastic, glass, and wire. Fill thicknesses generally range from approximately 6 feet to 23 feet; however, the maximum fill

thickness is approximately 40 feet (along the shoreline in the WDA). The groundwater at OU2 is tidally influenced and is generally brackish or saline.

The Supplemental RI Report finalized in March 2010 concluded that the main contaminants in soil at Sites 6 and 29 include metals (particularly lead), polycyclic aromatic hydrocarbons (PAHs), and polychlorinated biphenyls (PCBs), and the main contaminants in groundwater are metals [TtNUS, March 2010]. Contaminant fate and transport modeling and groundwater sampling conducted for OU2 indicated that migration of groundwater to the offshore was not anticipated to adversely impact the offshore. The additional investigation in 2007 and 2008 showed that DRMO contamination (lead and copper) was present in the backyards of Quarters S and N in the area referred to as the DRMO Impact Area, adjacent to the DRMO Storage Yard.

OU4 sampling activities that included collection of samples of soil eroding along the top of the Site 29 shoreline showed that the erosion was likely the cause of elevated metals (copper, lead, nickel) concentrations detected in offshore sediments [TtNUS, August 2005a; TtNUS, February 2006] (discussed further in Section 3.4). In 2002, a utility trench was excavated to place new utilities to service the Building 298 offices. The excavated soil was disposed of off yard, the trench was backfilled with clean fill material, and the trench is considered a clean area within the OU2 boundary.

A list of important OU2 historical events and environmental investigations with relevant dates in site chronology is shown below.

Event	Date
OU2 area filled with material excavated from Henderson's Point	1902 to 1905
DRMO activities began (stone crusher and scrap metal yard)	1920
Additional filling and disposal at OU2 (WDA)	1920 to 1975-1979
Onsite disposal ended with trash being taken off yard for disposal	1975 to present
Seawall constructed	1940s
Coal and coke storage facility located at Site 6 (Building 172)	1942 to 1957
Sandblast grit (unused) storage located at Site 6 (Building 172)	1957 to 1960
Teepee Incinerator (Building 290) operated and was demolished when operation ended	1965 to 1975
Building 298 used as industrial waste treatment facility	1975 to 1980s
Hose handling facility located at Site 29 (Building 310)	1980 to present
Pesticide handling conducted at Building 314	1982 to 1995

Event	Date
Open storage of batteries at DRMO discontinued	1983
Environmental sampling began at OU2 (as part of FCS)	1984
RFI and RFI Data Gap investigation conducted at Site 6 (including what is now Site 29)	1989 to 1992 and 1995
DRMO capped as an interim corrective measure	1993
Clean closure under RCRA of industrial waste treatment facility (Building 298)	1997
Portion of Site 6 separated into a new site (Site 29) and field investigation at Site 29 conducted	1998
Emergency Removal Action (shoreline stabilization) at Site 6	1999
Excavation for utility trench at Building 298 conducted	2002
Soil washing treatability study conducted	2005
Emergency Removal Action, including placement of shoreline controls, conducted at Site 29. Shoreline repairs completed in 2008.	2005 to 2006 2008
Surficial debris (including metal pieces and wires) removed from eastern portion of Site 29 with the area covered with gravel	2006
Additional Investigation at OU2 conducted to refine remedial options	2007 to 2008
Removal action conducted	2010
Pre-design investigation to complete delineation of contamination.	2011
OU2 Pre-Design Soil sampling conducted	April 2011
LUC Inspections	June 2013
Remedial Action (DRMO Storage Area and WDA)	July 2013 to August 2014

CERCLA Remedial Summary

Based on the results of the Supplemental RI Report, several human health risks were identified that require remedial action. In response to these risks, the Navy performed a removal action for the DRMO Impact Area to remove the potential unacceptable risks from OU2 contamination in the DRMO Impact Area. The removal action conducted in 2010 included excavation of contaminated soil from the DRMO Impact Area and offsite disposal, and site restoration activities were conducted in spring 2011. As documented in the September 2011 ROD and the December 2012 Final Construction Completion Report for DRMO Impact Area, no further action is required for the DRMO Impact Area. The September 2011 ROD for OU2 selected excavation and off-yard disposal of soil associated with potentially unacceptable risks to construction workers soil excavation with off-site

disposal for the DRMO Storage Area and WDA along with LUCs to restrict residential land use, minimize erosion, and prevent exposure to soil beneath Building 298 for all receptors. Remedial Action construction commenced during Summer 2013. Major activities and reports prepared for OU2 under CERCLA are presented below.

Document	Author/Date	Administrative Record Number
Final OU2 Supplemental RI Report	TtNUS, March 2010	001743
Final OU2 Pre-Design Sampling and Analysis Plan	TtNUS, November 2010	002513
Final OU2 FS Report	TtNUS, April 2011	002554
Final OU2 PRAP	Navy, July 2011	001689
Final OU2 ROD	Navy, September 2011	002620
Final OU2 LUCRD	Tetra Tech, March 2012	002673
Final OU2 Remedial Design	Tetra Tech, November 2012	002775
Final Remedial Action Work Plan (DRMO Area)	CB&I, July 2013	002946
Final Remedial Action Work Plan (WDA)	AGVIQ, August 2013	Not Yet Assigned
DRMO Impact Area		
Action Memorandum including EE/CA for Removal Action for DRMO Impact Area	Navy, November 2009	001351
Final Removal Action Work Plan for DRMO Impact Area	Shaw, May 2010	001746
Final Construction Completion Report for DRMO Impact Area	Shaw, December 2012	Not Yet Assigned

Activities Completed in FY 2014

Separate Remedial Action Work Plans were prepared and finalized for the DRMO Storage Area and the WDA in July and August 2013, respectively. Remedial Action commenced in the DRMO Storage Area in July 2013 and in the WDA in August 2013. Remedial Action construction activities are anticipated to be completed in Summer 2014. Preparation of the Construction Completion Reports for the DRMO Area and WDA will occur during Summer 2014.

CERCLA Path Forward

The CERCLA path forward for OU2 is as follows:

- Near Term Milestones
 - Construction Completion Reports (DRMO and WDA)
 - Long Term Management Plan
 - LUC Inspection

- Out Year Milestones
 - Long-term Management
 - Five-year reviews

The schedule for upcoming activities and milestones for OU2 is included in Attachment B.

3.3 Operable Unit 3 (OU3)

Site Description

OU3 consists of:

- Site 8 – Jamaica Island Landfill (JILF)
- Site 9 – Former Mercury Burial Sites (MBI and MBII)
- Site 11 - Former Waste Oil Tank Nos. 6 and 7

OU3 is located in the eastern portion of PNS (Figure 2) and consists of 22 acres currently used for parking, occupational uses, and recreational uses. Wetlands are located by Jamaica Cove to the north of OU3. The hazardous waste storage facility (Building 357) is located to the northeast of OU3, and the boundary of OU3 does include a portion of the paved area west of the building. To the east of OU3 is Clark Cove, and the solid waste storage facility (Building 337) is located to the south. The Automotive Hobby Shop (Building 320) and medical clinic (H1) are located to the west. The current features reflect post-remedial construction conditions (remedial construction detailed below).

The offshore area of OU3 is part of the Jamaica Cove and Clark Cove AOCs which were investigated as part of the EERA. Sampling locations in monitoring stations MS-5 through MS-9 in the Interim Offshore Monitoring Program are located within the intertidal and subtidal areas of Jamaica and Clark Coves. The offshore monitoring results are discussed as part of OU4 in Section 3.4.

Nature and Extent of Potential Contamination

Site 8 is the landfill (JILF), and Sites 9 and 11 are focused areas located within the JILF boundary. The Navy used the JILF, which previously consisted of tidal mudflats, as a disposal area from 1945

to 1978 for general refuse, trash, construction rubble, dredged sediment, and various industrial wastes. The boundary of the landfill defines the boundary of OU3. Mercury burial vaults (MBI and MBII) were placed in two locations within the landfill in the 1970s and then removed (intact) and disposed of off-site in the 1990s/early 2000 (Site 9). There is no evidence that mercury from the vaults has contaminated surrounding soil or groundwater. The waste oil tanks were used from 1943 to 1989 and were removed intact along with surrounding soil in 1989 (Site 11). Soil contamination remaining in the vicinity of Site 11 appeared to be landfill material (Site 8) mixed with petroleum hydrocarbons that may have originated from spills during filling of the tanks formerly at Site 11. Therefore, the soil contamination remaining in the vicinity of Site 11 is considered Site 8 contamination.

Environmental sampling began at OU3 in 1984, and over time has included various investigations of soil, groundwater, seeps, sediment sampling in the intertidal area, geophysical surveying, and test pitting. The OU3 ROD characterized Site 8 as containing a large volume of low-level hazardous materials [Navy, August 2001]. A variety of organic and inorganic constituents were detected in soil and groundwater and include volatile organic compounds (VOCs), semi-volatile organic compounds (SVOCs), PCBs, pesticides, metals, and petroleum hydrocarbons. Soil and groundwater data for Sites 8, 9, and 11 show similar chemical contamination throughout the area of the landfill. Low levels of dioxins were also detected during test pitting.

A list of important OU3 historical events and environmental investigations with relevant dates is shown below.

Event	Date
Use of underground storage tanks at Site 11 to store waste oil before offsite disposal began	1943
Landfilling of tidal flats east of Seavey Island and west - southwest of Jamaica Island began	1945
Poured concrete blocks and precast concrete pipes containing mercury-contaminated wastes buried in two locations (MBI and MBII) at the JILF	Between 1973 and 1975
Dredged sediment from the Dry Dock area disposed of at the JILF, and landfilling of the area discontinued	1978
IAS identifies the JILF and MBI and MBII as sites	1983
Environmental investigations began at OU3 (as part of the FCS)	1984
Use of tanks at Site 11 discontinued, and tanks and surrounding soil removed	1989
RFI and RFI Data Gap investigations conducted	1989-1992 and 1994

Event	Date
Pipe and blocks (three) removed from MBI and disposed of off site	1994 and 1997
Geophysical survey of OU3 conducted	1998
Blocks (eight) removed from MBII and disposed of off site	2000
Test pitting investigation conducted based on results of geophysical survey; 40 drums containing non-hazardous material located and removed	2000
Significant construction of remedy started	2002
Remedy construction completed	2004
OU3 Rounds 1 and 2 post-remedial OM&M conducted	2006
OU3 Rounds 3 and 4 post-remedial OM&M conducted	2007
OU3 Rounds 5 and 6 post-remedial OM&M conducted	2008
OU3 Rounds 7 and 8 post-remedial OM&M conducted	2009
OU3 Round 9 post-remedial OM&M conducted	April to June 2010
OU3 Round 10 post-remedial OM&M conducted	April 2011
OU3 Round 11 post-remedial OM&M conducted	May 2012
OU3 Landfill and LUC Inspection	May 2013, June 2014

CERCLA Remedial Summary

During the development of the RI/FS several human health risks were identified that required remedial action, primarily from metals and PAHs. In response to these risks, the selected remedy in the ROD for OU3 included installation of a RCRA Class C landfill cover and implementation of institutional controls, erosion controls, and monitoring [Navy, August 2001]. In addition, a 2003 ESD for the ROD described the addition of excavation and consolidation of material within the limits of the JILF before placement of the RCRA Class C landfill cover [Navy, September 2003]. Wetlands were constructed within the excavated area in 2003, and construction of the cap was completed in September 2004. Management of groundwater migration (formerly OU6, see Section 1.4) was combined into the OU3 remedy through a second ESD [Navy, October 2005]. The OM&M program for OU3 was initiated in July 2006, and 11 rounds of sampling and inspection have been completed through spring 2012.

Five-year reviews for OU3 are required since hazardous substances, pollutants, or contaminants remain on site at levels that do not allow for unlimited use and unrestricted exposure. The first

Five-Year Review Report for PNS was finalized in June 2007 [TtNUS, June 2007], and the second Five-Year Review Report for PNS was finalized on May 31, 2012. Major activities and reports prepared for OU3 under CERCLA are presented below.

Document	Author/Date	Administrative Record Number
Revised Risk Assessment for OU3	TtNUS, 2000	000922
Final FS for OU3	TtNUS, November 2000	000922
Final ROD for OU3	Navy, August 2001	001018
Final Phase I remedial design, evaluation of consolidation for MBII area and Jamaica Cove area, and Phase II remedial design	US Army, June and November 2002	001139, 001143, 001149, and 001195
Changes to OU3 ROD documented in ESDs	Navy, September 2003 and October 2005	001293 and 001493
Final Remedial Action Construction Report	TtEC, May 2006	001561
Final Post-remedial OM&M plan (without Land Use Control Remedial Design)	TtNUS, June 2006	001566 and 001567
First Five-Year Review Report	TtNUS, June 2007	001601
Final Rounds 1 through 4 evaluation report	TtNUS, July 2009	000910
Final Rounds 1 through 9 evaluation report	TtNUS, April 2011	002563
Final LUCRD	Navy, August 2011	002574
Final OU3 Post Remedial OM&M Plan (Revision 1, Vol. 1 & 2)	TtNUS, December 2011	002638 and 002639
Second Five-Year Review Report	Tetra Tech, May 2012	002697
Final Round 11 Data Package for Post Remedial OM&M Program	Tetra Tech, September 2012	002752
Draft Final Round 12 Data Package for Post Remedial OM&M Program	SDGC Group, April 2014	Draft Final Document
Final Gas Monitoring Probe Abandonment Plan	SDGC Group, June 2014	Not Yet Assigned

Activities Completed in FY 2014

Inspection (Round 13) of the landfill and LUCs was completed in May 2014. A Gas Monitoring Probe Abandonment Plan was prepared, and the final document was submitted in June 2014. Per agreement between the Navy, EPA, and MEDEP in December 2012, annual landfill gas sampling and groundwater sampling for arsenic are discontinued for future sampling and inspection events.

CERCLA Path Forward

The CERCLA path forward for OU3 is as follows:

- Near Term Milestones
 - LUC Inspection and Landfill Inspection
 - Remedial Action Completion Report (RACR)
- Out Year Milestones
 - Long-term Management
 - Five-year reviews

The schedule for upcoming activities and milestones for OU3 is included in Attachment B.

3.4 Operable Unit 4 (OU4)

Site Description

OU4 is the offshore area of the Piscataqua River and the Back Channel around PNS and consists of Site 5 (Former Industrial Waste Outfalls) in addition to areas offshore of PNS that potentially were affected by PNS onshore ERP sites as shown on Figure 2. Site 5 is located within the Dry Docks AOC and consisted of numerous discharge points along the Piscataqua River in the berth area by the dry docks in the western end of PNS. Site 5 had offshore impacts without any onshore impacts. Maintenance dredging is conducted periodically in the berth areas in the Dry Docks AOC. Onshore OUs with sites that have potential offshore impacts are OU1 (Section 3.1), OU2 (Section 3.2), OU3 (Section 3.3), OU7 (Section 3.5), OU8 (Section 3.6), and OU9 (Section 3.7).

Nature and Extent of Potential Contamination

The outfalls associated with Site 5 were used from approximately 1945 to 1975 to discharge liquid industrial wastes (primarily from acidic, alkaline, and metal-plating rinse baths) to the offshore. The wastewaters may have contained heavy metals (mercury, lead, cadmium, chromium, copper, and zinc), oils and grease, and PCBs. Lead sediment from decommissioned batteries (as part of operations at Site 10) was also reportedly included in the discharges to the river before 1975 [Weston, June 1983].

The EERA identified near-shore habitats adjacent to PNS that may have been affected by onshore ERP sites as AOCs, including Clark Cove, Sullivan Point, DRMO Storage Yard, Dry Docks, Back Channel, and Jamaica Cove [NCCOSC, May 2000; Johnston, et. al., December 1994].

An Interim ROD for OU4 was signed in May 1999 that required the Navy to conduct an interim remedy and offshore monitoring for OU4 until a final remedy is implemented [Navy, May 1999]. The Interim Offshore Monitoring Plan (Revision 0), was finalized in October 1999 and updated (Revision 1) in November 2010. The monitoring plan specifies the sampling locations, analytical program, and frequency of sampling. The Interim Offshore Monitoring Program includes 14 monitoring stations in the PNS offshore AOC areas, as shown on Figure 5. The monitoring program began in 1999 and initially included sediment, mussel, and juvenile lobster sampling and analysis [TtNUS, October 1999]. The data from Rounds 1 and 2 were used to develop PRGs for OU4 that are being used as Interim Remediation Goals (IRGs) for making decisions as part of the Interim Offshore Monitoring Program [TtNUS, November 2001]. Evaluation of the data from Rounds 1 through 4 resulted in changes to the Interim Offshore Monitoring Program [TtNUS, July 2002], including to discontinue select analyses for sediment (acid volatile sulfides and simultaneously extracted metals), discontinue juvenile lobster sampling, and only conduct subsequent sampling (starting with Round 5) during late summer. Additional evaluation based on Rounds 1 through 7 recommended that only sediment be sampled during Rounds 8 and 9 (no mussel sampling) and to discontinue alkylated PAH analysis for sediment samples. The Navy prepared an update (Revision 1) to the Interim Offshore Monitoring Plan [TtNUS, November 2010] for monitoring subsequent to Round 10 which concluded that monitoring is no longer required at several monitoring stations, as discussed below. Round 11 was completed in April 2011. A description and current status of each monitoring station is provided below.

- **MS-01:** This monitoring station was located in the western portion of the Back Channel AOC, offshore of Site 34 (OU9). In 2007, a non-time-critical removal action was conducted for source material at Site 34, and additional sediment sampling at MS-01 was conducted in August 2009 to determine the extent of PAH contamination. Rounds 8, 9, and 10 sampling were not required for MS-01, but monitoring of sediment for PAHs was conducted at this station during Round 11.
- **MS-02 and MS-10:** These monitoring stations were located in the Back Channel and Sullivan Point AOCs, respectively, and are not located immediately offshore of any ERP sites. In accordance with the 2010 Interim Offshore Monitoring Plan, interim offshore monitoring was discontinued at these stations and no additional offshore actions are needed for these stations because chemical concentrations in sediment are less than IRGs, and the data do not indicate any impacts from known ERP sites.
- **MS-03 and MS-04:** These monitoring stations were located in the eastern portion of the Back Channel AOC, offshore of Site 32 (OU7). Elevated metals concentrations have been detected at

these stations, and foundry slag associated with Site 32 has been identified in the intertidal areas and is likely the source of the elevated metals concentrations at these stations. In June 2006, a time-critical removal action was conducted to provide shoreline erosion controls where significant erosion of the shoreline was occurring. Surficial debris (including slag) was removed from the shoreline, and shoreline controls were placed along the entire Site 32 shoreline in the mid- to high-tide area. Additional sampling was conducted in 2008 as part of Phase II RI field work for OU7 to determine the extent of copper and PAH contamination in sediment [TtNUS, July 2011]. Rounds 8, 9, and 10 sampling were not required for these monitoring stations. Monitoring of sediment for PAHs and copper was conducted at this station during Round 11.

- **MS-05, MS-06, MS-07, MS-08, and MS-09:** MS-05 and MS-06 were located in the Jamaica Cove AOC. MS-07, MS-08, and MS-09 were located in the Clark Cove AOC. MS-05, MS-08, and MS-09 are immediately offshore of OU3, and MS-06 and MS-07 are in the offshore area adjacent to OU3. An increase in chemical concentrations was identified within MS-05 and MS-09 after OU3 remedial action construction, and additional scrutiny investigation was conducted to delineate the area of elevated chemical concentrations in these two stations [TtNUS, February 2010], and additional sampling (during Rounds 8, 9, and 10) was conducted for MS-05, MS-08, and MS-09 to evaluate concentration trends post-remedial action. Chemical concentrations in sediment at MS-05, MS-08, and MS-09 during the recent sampling events were less than IRGs. MS-06 and MS-07 have not had exceedances of IRGs, indicating that sediment in the offshore area adjacent to OU3 has not been impacted by OU3. Monitoring of sediment for PAHs and metals at MS-05 and for PAHs, 4,4'-DDT, dioxins/furans, PCBs, and metals at MS-08 and MS-09 was conducted during Round 11. Sediment at MS-07 also was monitored during Round 11 as a reference station for MS-08 and MS-09. In accordance with the 2010 Interim Offshore Monitoring Plan, interim offshore monitoring was discontinued at MS-06.
- **MS-11:** This monitoring station was located in the DRMO Storage Yard AOC offshore of OU2. Erosion of metals-contaminated soil along a portion of the OU2 shoreline (by Site 6) was identified in 1999, and a time-critical removal action was conducted to prevent further erosion of contaminants by placing shoreline erosion controls along a portion of the OU2 shoreline. The entire OU2 shoreline currently has some type of shoreline erosion controls following a time-critical removal action conducted in 2005 and 2006, and subsequent repairs in 2008, to provide shoreline erosion controls along the remaining portion of the OU2 shoreline (at the Site 29 shoreline). Sediment is present at only one location at MS-11 (on the eastern side of the monitoring station); the sediment concentrations at the other two locations (for comparison to IRGs) were estimated using mussel data from those locations. Additional scrutiny was conducted to confirm that

elevated concentrations of metals (copper, lead, and nickel) in MS-11 sediment on the eastern side of the monitoring station were likely from erosion from OU2 [TtNUS August 2007]. Rounds 8, 9, and 10 sampling were not required for MS-11. Monitoring of sediment for copper, lead, and nickel was conducted at the location on the eastern side of this station during Round 11.

- **MS-12:** This station was located in the Dry Dock AOC offshore of Site 10 (OU1). One industrial waste outfall (Site 5) historically discharged into the offshore area of Site 10 prior to 1975, likely with wastewater from Site 10 operations. There are no current ERP sources to MS-12. Groundwater data from Site 10 do not indicate that lead in soil is leaching to groundwater at concentrations that would adversely impact the off shore, and PAHs are not chemicals associated with the Site 10 source. The elevated levels of lead and/or PAHs at MS 12 may be caused by a combination of sources that may or may not be related to PNS, including potential migration or transport from ERP sites, discharges from barges/boats, discharges from storm water outfalls located in the vicinity of the shipyard, and dock-side activities. Additional scrutiny was required for MS-12 to determine the extent and potential sources of contamination [TtNUS, February 2010]. Rounds 8, 9, and 10 sampling were not required for MS-12. Monitoring of sediment for PAHs and lead was conducted at this station during Round 11.
- **MS-13 and MS-14:** These stations were located in the Dry Dock AOC to monitor sediment potentially impacted by Site 31 (OU8). Industrial waste outfalls (Site 5) historically discharged in this area prior to 1975. The area by MS-13 was dredged between January and April 2002 (between Rounds 5 and 6). Potential sources of PAHs detected in sediment at these stations that may or may not be related to PNS include potential migration or transport from ERP sites, discharges from barges/boats, discharges from storm water outfalls located in the vicinity of the shipyard, and dock-side activities. Round 8 sampling was required for these monitoring stations; additional scrutiny was not required. PAH concentrations in most samples were less than IRGs. No additional monitoring or action are needed at these stations because of infrequent number of exceedances of IRGs over the eight rounds of sampling and because the data do not indicate any impacts from ERP sites. In accordance with the 2010 Interim Offshore Monitoring Plan, interim offshore monitoring was discontinued at these stations.

A list of important OU4 historical events and environmental investigations with relevant dates is shown below.

Event	Date
Outfalls in the Dry Dock area were used to discharge industrial wastes into the Piscataqua River	~1945 to 1975
Sanitary and storm sewer systems separated; industrial discharge through outfalls discontinued	Completed by 1975
Industrial waste outfalls first identified as a site and operations that previously discharged to the outfalls are identified (as part of the IAS)	1983
Environmental sampling began including the offshore (as part of FCS)	1984
Phase I and Phase II offshore sampling for offshore human health and ecological risk assessments conducted	1991 to 1993
Interim offshore monitoring conducted (11 Rounds) and additional scrutiny investigation	1999 to 2011
Round 12 Interim Off-Shore/Pre-Removal Sediment Confirmation Sampling	Fall 2013

Various removals conducted by the Navy at different on-shore sites have contributed to decreases in chemical concentrations in sediment. Based on assessment of all sediment sampling results, nine stations indicated acceptable concentrations (MS-02, -05, -06, -07, -08, -09, -10, -13, and -14), and no further action is required for these stations. The monitoring stations where unacceptable concentrations were identified include MS-01 (off-shore of OU9), MS-03 and MS-04 (off-shore of OU7), MS-11 (off-shore of OU2), and MS-12 (associated with a former Site 5 outfall).

CERCLA Remedial Summary

Environmental investigations and risk assessment identified several human health and ecological risks. An Interim ROD for OU4 was signed in May 1999 that requires the Navy to conduct an interim remedy for OU4 and interim offshore monitoring until a final remedy is implemented [Navy, May 1999]. The Interim Offshore Monitoring Plan, Revision 0, was finalized in October 1999 and updated (Revision 1) in November 2010, and the monitoring plan specifies the sampling locations, analytical program, and frequency of sampling. The OU4 FS and Proposed Remedial Action Plan were finalized in September 2012 and February 2013, respectively. The Record of Decision for OU4 was signed in August 2013, with the selected remedy being sediment removal with off-yard disposal for stations MS-01, MS-03, MS-04, and MS-12. Major activities and reports prepared for OU4 under CERCLA are presented below.

Document	Author/Date	Administrative Record Number
Final HHRA Report for Offshore Media	McLaren/Hart, May 1994	000229
Final Interim ROD for OU4, interim offshore monitoring plan, and first round of sampling	Navy, May 1999 and TtNUS October 1999	000676 and 000750
Final EERA document	NCCOSC, May 2000	000838
PRGs for OU4	TtNUS, November 2001	001062
Baseline evaluation of first four rounds of interim offshore monitoring data	TtNUS, July 2002	001150
Evaluation of first seven rounds of interim offshore monitoring data, and stations requiring additional scrutiny and/or additional monitoring (as part of Rounds 8 and 9)	TtNUS, November 2004	001416/ 001417
Final Work plan (QAPP) for additional scrutiny investigation and Round 8 and additional scrutiny investigations	TtNUS, August 2005	001484
Additional scrutiny investigation report and work plan for second phase of additional scrutiny	TtNUS, August and September 2007	001612 and 001619
Final Evaluation report for first 10 rounds	TtNUS, February 2010	001716
Final Interim Offshore Monitoring Plan updated (Revision 1)	TtNUS, November 2010	002514
Final FS Report	Tetra Tech, September 2012	002749
Final OU4 ROD	Navy, August 2013	002897
Final Sampling and Analysis Plan for Pre-Removal Sediment Confirmation Sampling	Tetra Tech, September 2013	002924
Draft Pre-Removal Confirmation Sediment Sampling Report	Tetra Tech, April 2014	Draft Document
Draft Remedial Action Work Plan	AGVIQ, June 2014	Draft Document

Activities Completed in FY 2014

The ROD for OU4 was signed on August 15, 2013. A Sampling and Analysis Plan for pre-design sediment sampling was finalized in September 2013, and sediment sampling was performed in November and December 2013 to better delineate areas for sediment removal. The draft Pre-Removal Confirmation Sediment Sampling Report was submitted in April 2014 and presents the results and recommendations from the Fall 2013 sediment sampling. The Remedial Action Work Plan will be submitted in Summer 2014. The Remedial Action consisting of sediment removal and off-site disposal is scheduled to commence in Fall 2014.

CERCLA Path Forward

The CERCLA path forward for OU4 is as follows:

- Near Term Milestones
 - RD/RA
- Out Year Milestones
 - Remedial Action Completion Report (RACR)

The schedule for upcoming activities and milestones for OU4 is included in Attachment B.

3.5 Operable Unit 7 (OU7)

Site Description

OU7 consists of:

- Site 32 – Topeka Pier Site

Site 32 encompasses approximately 17 acres of filled land on the northern shore of PNS, along the Back Channel of the Piscataqua River, from just west of Building 162 to east of former Building H29 and from the Back Channel south to Building 129 (Figure 2). The land is currently used for office parking (about 35 percent of the site area), equipment storage, vehicle and rail car maintenance, transducer repair, boat launch, temporary housing for Navy personnel (H23), and medical clinic (H1). The pier and offshore areas of OU7 are used for docking of boats.

The offshore area of OU7 is part of the Back Channel AOC which was investigated as part of the EERA. Sampling locations within monitoring stations MS-03 and MS-04 were located in the intertidal and subtidal area along the OU7 shoreline [TtNUS, November 2004, February 2010, November 2010]. The offshore area is discussed as part of OU4 in Section 3.4.

Nature and Extent of Potential Contamination

Topeka Pier was constructed in the Back Channel of the Piscataqua River to dock the prison ship USS Topeka. Storing and milling of lumber in the area began by 1910, and a timber basin was established at the southeastern corner of the site. The area west of the timber basin was used to store coal, wood, and scrap iron. Combustibles including paints and oils were stored in Building 98.

VOCs, SVOCs, pesticides, PCBs, dioxins, furans, and inorganics were detected in surface and subsurface soil samples. The average concentrations of chemicals in the fill area without debris in the vicinity of former Building 237 were determined to be statistically less than the average concentrations for the rest of OU7 [TtNUS, July 2011]. Inorganics and SVOCs in a small number of samples were detected in groundwater.

A list of important OU7 historical events and environmental investigations with relevant dates is shown below.

Event	Date
Filling of area conducted, including connecting Dennett's and Seavey Islands	1900 to 1945
Lumber storage and milling began (in southeastern corner of Site 32)	1910
Various buildings constructed to accommodate the increased demand for lumber during World War I, including a sawmill (Building 129), a lumber storehouse with timber racks (Building 132), and an additional lumber storehouse (Building 149)	Prior to 1920
Many current buildings built (to support World War II)	1941 to 1945
Wastes from buildings discharged to river; discontinued when sanitary sewer system installed	1940s to 1970s
Building 306 constructed as a transducer repair facility	1980
Excavation work along Goodrich Avenue and near Building H23 uncovered debris in area including large dry-cell batteries, graphite electrodes, brick, wood, metal pipe and wire, glass, asbestos cloth, and crucibles used in foundry operations. Site 32 identified as SSA	1994 to 1995
SSI and geophysical survey conducted	1998
SSI recommended RI	2000
Phase I RI field work conducted	2003
Parking area repaved	2003/2004
Emergency removal action (shoreline stabilization) conducted	June 2006
Phase II RI field work conducted	2008

CERCLA Remedial Summary

The RI identified several human health risks, and the FS report finalized in June 2013 evaluated remedial alternatives. The Proposed Remedial Action Plan was finalized in July 2013. The ROD for OU7 was signed in September 2013, with the selected remedy of removing contaminated soil from two areas within the Former Timber Basin and LUCs to prevent residential land use. Major activities and reports prepared for OU7 under CERCLA are presented below.

Document	Author/Date	Administrative Record Number
Final SSI Report	TtNUS, May 2000	000812
Final RI Report	TtNUS, July 2011	002634
Final FS Report	Tetra Tech, June 2013	002842
Final PRAP	Tetra Tech, July 2013	002851
Final ROD for OU7	Navy, September 2013	002925
Draft LUCRD	Tetra Tech, December 2013	Draft Document

Activities Completed in FY 2014

The final PRAP for OU7 was submitted in July 2013. A 30 day public comment period was open from July 16, 2013 to August 14, 2013, and the Navy held a public hearing at the Kittery Town Hall on July 23, 2013. The ROD for OU7 was signed on September 30, 2013. The draft LUCRD was submitted in December 2013 and will be finalized and filed with the appropriate municipal land use offices in Kittery, ME and Portsmouth, NH in 2014. The draft Remedial Action Work Plan will be submitted during Summer 2014.

CERCLA Path Forward

The CERCLA path forward for OU7 is as follows:

- Near Term Milestones
 - RA
- Out Year Milestones
 - Long Term Management
 - Five-year reviews

The schedule for upcoming activities and milestones for OU7 is included in Attachment B.

3.6 Operable Unit 8 (OU8)

Site Description

OU8 consists of:

- Site 31 – Former West Timber Basin.

OU8 is a paved area located in the CIA, in the northwestern portion of PNS (Figure 2). OU8 is an industrial area surrounded by buildings or dry docks. The main site features were associated with the former plate yard, which was a fenced area with railroad spurs. Building 92 located east of the former plate yard is the Structural Shop. The former plate yard office (Building 157) was demolished in 2006.

The offshore area near OU8 is part of the Dry Dock AOC which was investigated as part of the EERA. Sampling locations within monitoring stations MS-13 and MS-14 in the Interim Offshore Monitoring Program were located adjacent to Dry Dock No. 1 to the east and east of Dry Dock No. 3, respectively (Figure 5). The offshore area is discussed as part of OU4 in Section 3.4.

Nature and Extent of Potential Contamination

During the early 1900s, wood for shipbuilding was stored and seasoned in the West Timber Basin (Site 31). A metal washing plant (Building 110) for the recovery of metals from the ash and skimmings of the brass foundries on the Shipyard was erected on the northern side of Site 31, and by-products from the plant were reportedly discarded into the timber basin. In addition, by-products from smelting and pigging (the process of pouring melted iron from a form into a mold) operations at the Shipyard were deposited into the timber basin. In 1940, a new plate yard was constructed near the quay wall and was active until 1960, serving as the primary steel storage yard and pickling location at the Shipyard.

Environmental sampling at OU8 was conducted as part of the Site Screening Investigation (SSI) in 1998 [TtNUS, May 2000] to determine the presence or absence of contamination and to determine whether further investigation under CERCLA was needed for the site. The investigation showed that fill material varies in thickness from 8.5 to 17.5 feet across the site and consists mostly of sand, silt, and rock fragments, with trace amounts of brick and other debris. In addition, a wedge of coal, cinders, and ash (approximately 8 feet thick, starting around 2 to 4 feet below ground surface) exists in the northern part of the site, tapering to the south to less than one foot thick. Groundwater at OU8 appears to be tidally influenced and ranges from saline/brackish along the perimeter of the site to fresh/mildly brackish further inland. Chemicals detected in site soils were PAHs and metals.

A list of important OU8 historical events and environmental investigations with relevant dates is shown below.

Event	Date
Wood storage and seasoning for shipbuilding conducted in West Timber Basin	Early 1900s to 1913
Filling of West Timber Basin began	1916
Quay wall installed to enclose the basin	1917
Metal washing plant (Building 110) constructed	1920s
Filling of basin enclosed by quay wall with rock, soil, cinders, and other waste and scrap material.	1920 to 1940
Buildings 110, 51 (acetylene plant and former pitch plant), and 83 (latrine) razed, pickling tanks adjacent to Building 110 removed, and train tracks constructed	1940
Building 92 extended over a portion of timber basin	1940
Plate yard with pickling tanks and washing aprons active	1940 to 1960
Pickling tanks removed after use of plate yard discontinued	Unknown (after 1960)
SSI conducted	1998
Removal of surface features and initial construction activities associated with expansion of Building 174	September to December 2006

CERCLA Remedial Summary

Based on the results of the 2000 SSI report, the site was recommended for further investigation. The SSI identified several contaminants of concern that exceed residential and/or industrial risk-based screening levels. Remedial Investigation activities will be initiated in 2014. Major activities and reports prepared for OU8 under CERCLA are presented below.

Document	Author/Date	Administrative Record Number
Final SSI Report	TtNUS, May 2000	00812
Draft RI Sampling and Analysis Plan	Tetra Tech, April 2014	Draft Document

Activities Completed in FY 2014

Significant military construction (MILCON) activities were completed within OU8 from 2011 through 2013, particularly for Building 174. The Navy submitted the draft RI Sampling and Analysis Plan in

April 2014 to complete additional investigation. Field sampling activities are anticipated to commence in 2014.

As part of the preparation of the draft RI Sampling and Analysis plan, it was proposed to modify the OU8 boundary based on actual locations of quay walls on east, south, and west sides of timber basin and building/historical shoreline on northern side using GPS coordinates of the sea wall recorded during construction and historic maps.

CERCLA Path Forward

The CERCLA path forward for OU8 is as follows:

- Near Term Milestones
 - RI Sampling and Analysis Plan
 - RI (field investigation and reporting)
 - FS
- Out Year Milestones
 - PRAP / ROD

The schedule for upcoming activities and milestones for OU8 is included in Attachment B.

3.7 Operable Unit 9 (OU9)

Site Description

OU9 consists of:

- Site 34 – Former Oil Gasification Plant, Building 62

OU9 is located in the central portion of PNS (Figure 2). The buildings at and in the vicinity of OU9 are used for industrial and commercial uses. Paved areas within OU9 are used for parking. Building 62 and its annex currently are used by the NAVFAC Mid-Atlantic Public Works Department as a mini-bulldozer shop and for storage. OU9 is in a historic district at PNS, and buildings at and near the site (Buildings 40, 43, 60, and 62) are considered contributing elements to the National Registry District [Louis Berger Group, April 2003]. There is a small, relatively flat grassy area within OU9. North of Building 62 Annex and northeast of Building 62 generally the area slopes gently north towards the roadway and then slopes steeply (i.e., forms ledges) to the water's edge at the

shoreline adjoining the Back Channel of the Piscataqua River. Access to the shoreline from the site is difficult because of the rapid changes in terrain at the ledges.

Nature and Extent of Potential Contamination

Combustion of coal and conversion of kerosene to illuminating gas were performed at the Former Oil Gasification Plant (Building 62) from the 1870s to early 1900s. Ash was generated from the oil gasification process and blacksmith shop which operated from 1915 to 1930. Ash was deposited primarily north of Building 62 and resulted in an ash pile that was removed in 2007. Pesticide storage activities were also conducted in Building 62.

A list of important OU9 historical events and environmental investigations with relevant dates is shown below.

Event	Date
Ash was generated during coal (fuel) combustion as part of oil gasification process	1870s to early 1900s
Ash was generated during coal (fuel) combustion as part of blacksmithing operation	1915 to 1930
Building 62 reportedly gutted by fire	1919
Shipyards Public Works Department uses Building 62 for storage	1930 to Present
Pesticides stored at Building 62	1960s to 1985
Site identified as SSA, and six drums of ash removed from pile (less than 2 cubic yards) removed from pile north of Building 62	1998 and 1999
Soil and sediment sampling	1998 and 2003
SSI conducted and extent of ash investigated	2004
Public comment period held	2005
Removal action conducted	2007
RI sampling conducted	2009 and 2010

High concentrations of PAHs and metals are associated with the presence of ash in site samples. Concentrations of PAHs and metals are typically low in samples without ash. The visual presence of ash was used to define the approximate extent of contamination as part of the 2004 investigation. The depth to the bottom of the deepest ash layer was five feet below grade, and typically significant reductions in concentrations were observed with depth beneath the deepest ash layer.

Based on data from temporary wells (installed and subsequently abandoned), no overburden groundwater is present at the site. The depth to bedrock varies from five to 12 feet.

CERCLA Remedial Summary

An RI was recommended for Site 34 to assess the potential risks based on the results of the SSI [TtNUS, August 2004]. Based on the results of the SSI, several human health risks were identified from exposure to ash material at the site. In response to these risks, an EE/CA was completed in 2005 that recommended excavation and offsite disposal of the ash pile and ash exposed at shoreline ledge areas [TtNUS, September 2005], and a non-time-critical removal action to implement these recommendations was completed in 2007. The Navy recommended that a removal action be performed before the RI because PAH and metals concentrations in the ash material were much greater than risk screening levels and would result in potentially unacceptable risks if the ash were uncovered. The 2007 ash removal action addressed nearly all unacceptable risks at the site since the majority of contamination at the site appeared to be associated with ash material. The RI evaluated residual site-related risks after removal of the ash. The FS report, finalized in May 2013, evaluated remedial alternatives. The Proposed Remedial Action Plan was finalized in July 2013. The ROD for OU9 was signed in September 2013, with the selected remedy of LUCs to prevent residential land use for the area north of Building 62, prevent residential land use of Building 62 Annex, and prevent unrestricted exposure for current industrial users to the subsurface beneath the floor of Building 62 Annex. Major activities and reports prepared for OU9 under CERCLA are presented below.

Document	Author/Date	Administrative Record Number
Final EE/CA for Site 34	TtNUS, September 2005	001495
Final Action memorandum for removal action	Navy, February 2007	001532
Final Removal action design	June 2007	001604
Removal action construction report	Shaw, July 2008	001670
Final RI Work Plan	TtNUS, July 2009	001744
Final RI Report	Tetra Tech, June 2012	002700
Final FS Report	Tetra Tech, May 2013	002840
Final PRAP	Tetra Tech, July 2013	002863
Final ROD for OU9	Navy, September 2013	002926
Draft LUCRD	Tetra Tech, December 2013	Draft Document

Activities Completed in FY 2014

The final PRAP for OU9 was submitted in July 2013. A 30 day public comment period was open from July 16, 2013 to August 14, 2013, and the Navy held a public hearing at the Kittery Town Hall on July 23, 2013. The ROD for OU9 was signed on September 30, 2013. The draft LUCRD was submitted in December 2013 and will be finalized and filed with the appropriate municipal land use offices in Kittery, ME and Portsmouth, NH in 2014.

CERCLA Path Forward

The CERCLA path forward for OU9 is as follows:

- Near Term Milestones
 - LUCRD
- Out Year Milestones
 - LUC Inspections
 - Five Year Reviews

The schedule for upcoming activities and milestones for OU9 is included in Attachment B.

3.8 Site Screening Area

Site Description

The Site Screening Area (SSA) is a study area at PNS under investigation to determine whether further action as part of an RI/FS is needed. The SSA consists of:

- Site 30 – Galvanizing Plant, Building 184

Site 30 is located in the central portion of PNS (Figure 2). Building 184 was vacated in 2010 and will be remodeled for occupation by Autonomous Underwater Vehicle personnel. Prior to 2010, Building 184 was used for industrial purposes (welding school) and is a historically significant building [Louis Berger Group, April 2003]. The surrounding buildings are commercial and industrial.

Nature and Extent of Potential Contamination

Building 184 was constructed in 1943 as a galvanizing plant. After World War II, Building 184 was converted from a galvanizing plant to the Shipyard's electrical testing laboratory. The building was used as a welding school from the early 1960s until 2010. Little information is available about the

specific types and quantities of chemicals used throughout the history of Building 184. Chemicals associated with galvanizing and other industrial operations similar to those performed in Building 184 include caustic solutions (sodium hydroxide, sodium carbonate, trisodium phosphate, and tetrasodium pyrophosphate), acid solutions (hydrochloric and sulfuric), and flux solutions (sodium silicate). Tanks were used for metal parts assembly and were filled with various chemicals including large amounts of sulfuric acid, trisodium phosphate, alcohol, and acetone [Navy, January 2006]. With the changes in usage of Building 184, the use of the tank vault also changed, and it has been covered and uncovered several times.

Environmental investigations at Site 30 indicated that soil and groundwater sampled outside the building were not impacted by any potential environmental releases from the tank vault inside the building. However, additional investigation activities were recommended at the former tank vault within Building 184. Test pitting activities, conducted in 2001, indicated the presence of chemicals that are likely residuals from the cleaning operations. In addition, water was observed in the tank vault. Based on differences in elevations between the vault water and groundwater in monitoring wells outside the building, the water in the tank vault is likely not hydraulically connected to site groundwater. The building does not have gutters or downspouts, so it is likely that ponding of water against the brick outer wall of the building seeps through the masonry.

Based on site conditions, the Navy determined that a non-time-critical removal action was appropriate for the tank vault at Site 30 to mitigate environmental hazards to human and environmental receptors before determining whether an RI/FS is necessary. As described in the 2005 EE/CA, a removal action was completed that included regrading the area outside Building 184 to eliminate stormwater ponding along the wall adjacent to the tank vault in addition to periodic scraping and appropriate disposal of a crystalline substance growing along the eastern wall boundary with the tank vault. A follow-up EE/CA, in 2010, recommended removal of the tank vault.

A crystalline substance has been observed along eastern edge of the tank vault and in other areas of the building not associated with the tank vault. The crystalline substance was first observed in 1973 and again in 1994 and 1996. The crystals had a low pH (around 1.0 or 2.0) and were composed of predominantly sulfate and metals. The material was not hazardous based on Toxicity Characteristic Leaching Procedure (TCLP) characteristics but may be hazardous based on the RCRA corrosivity criterion because of the caustic nature of the crystals [Navy, January 2006]. It had been assumed that water coming in contact with crystalline materials within the tank vault was the cause of the crystalline growth along the outside edges of the tank vault. However, crystalline materials

are still present following the Removal Action. Additional sampling of the crystalline material was performed for crystallography analysis in April 2012.

A list of important Site 30 historical events and environmental investigations with relevant dates is shown below.

Events	Date
Building 184 constructed as galvanizing plant (acid proof vault used)	1943
Building 184 converted to an electrical testing facility (vault covered)	1946
Building 184 converted to clean room facility for cleaning metals parts (vault uncovered and used)	Between 1954 and 1956
Building 184 used as welding school (tank vault covered with concrete floor)	Early 1960s to 2010
Crystalline substance observed along edge of vault	1973
Crystalline substance observed and analyzed	1994 and 1996 to 1997
SSI conducted	1998
Test pitting within tank vault, and samples of fill material and crystalline substance analyzed	2001
Periodic removal of crystalline material by Shipyard	1997 to 2006
Removal of crystalline material and covering of affected area	2006
Regrading and paving conducted to redirect storm water runoff away from Building 184	2007
Removal Action completed	2011

CERCLA Remedial Summary

Environmental investigation identified the potential for exposure to human and environmental receptors to hazardous substances. In response to these potential risks, a removal action was completed in 2011. Following the removal action, a No Further Action Decision document was finalized in March 2014. Major activities and reports prepared for Site 30 under CERCLA are presented below.

Document	Author/Date	Administrative Record Number
Final SSI Report	TtNUS, May 2000	000812
Final EE/CA for Site 30 (Revision 1)	TtNUS, August 2005	001485

Document	Author/Date	Administrative Record Number
Final Action memorandum for non-time-critical removal action	Navy, January 2006	001522
Final EE/CA (Revision 2) for tank vault removal	TtNUS, October 2010	002503
Final Action Memorandum (Revision 2) for tank vault removal	Navy, December 2010	002518
Final Removal Action Work Plan	Shaw, July 2011	002518
Final Construction Completion Report	CB&I, November 2013	002939
Final No Further Action Decision Document	Navy, March 2014	002987

Activities Completed in FY 2014

The Final Construction Completion Report, submitted in November 2013, summarizes the Removal Action that was completed in Fall 2011 to remove the fill material in the Site 30 vault. The No Further Action Decision Document was finalized in March 2014, and a public comment period was held for the Draft Final document from January 7 to February 6, 2014. EPA and MEDEP provided letters of concurrence on the Final No Further Action Decision Document.

CERCLA Path Forward

No further action under CERCLA is required for Site 30.

4.0 SITE RANKING

A relative risk ranking was conducted from 1995 to 1999 prior to the signing of the FFA to assist in prioritizing site cleanups. Using the DoD developed Relative Risk Site Evaluation framework, sites are categorized into High, Medium, and Low relative risk groups based on an evaluation of contaminants, pathways, and human and ecological receptors. Each of these environmental media are evaluated using three factors: the contaminant hazard factor (CHF), the migration pathway factor (MPF), and the receptor factor (RF). Upon determination of the CHF, MPF, and RF a decision matrix was utilized to determine the category of relative risk for each media as High, Medium, or Low. The relative risk category for a site is determined from the highest rating resulting from the evaluation of the three media. A site's rating may change based on new or additional information or as a result of remediation activities. Site that were determined to be NFA prior to the signing of the FFA were not included in the risk ranking.

Table 4 presents a summary of relative risk ranking results determined prior to the FFA and which sites have had remediation activities completed or proposed and where LUCs have been implemented.

5.0 SCHEDULES

In accordance with the FFA (Section 12), as part of the annual SMP update, schedules are developed for each site at PNS showing proposed activities for the FY 2015 and FY 2016 (FY+1). In addition, activities completed or scheduled in FY 2014 are also presented. Schedules are developed using the current status of activity anticipated and projected funding availability. Line item durations were developed using durations for specific process activities provided in the FFA. Schedules for OU1, OU2, OU3, OU4, OU7, OU8, OU9, and Site 30 are attached as Attachment B.

All FFA "deliverables" required during the cleanup process are included. Primary documents are prepared by the Navy and include draft and draft final submission and review by USEPA and MEDEP, as necessary. Responses to comments on the draft document are prepared by the Navy. If comments are not received on the draft final version, it becomes the final document. If comments are received on the draft final document, the Navy will make the necessary modifications and issue the final Primary Document. Secondary documents, as listed in the FFA, also undergo review; however, a draft final version is not provided. The FFA (Section 10.0) defines review, response and revision time frames for Primary and Secondary documents.

6.0 LAND USE PLANNING

As an active Navy facility, PNS is subject to ongoing operations, maintenance, and improvements. Based on anticipated site use and receptors, LUCs have been implemented at some ERP sites to be protective where contamination has been left in place. In order to maintain protectiveness of human health, the environment, and the implemented remedy, it is crucial to identify and communicate which areas at PNS are subject to LUCs. The Sites with LUCs in place are:

- Site 10 – Former Battery Acid Tank No. 24 (OU1)
- Site 6 – DRMO Storage Yard (OU2)
- Site 29 – Former Teepee Incinerator Site (OU2)
- Site 8 – Jamaica Island Land Fill (OU3)

For two additional Sites, draft LUCRDs were submitted for regulatory review in December 2013, and LUCs are anticipated to be finalized during 2014.

- Site 32 – Site 32 - Topeka Pier Site
- Site 34 – Former Oil Gasification Plant, Building 62

This information is made available on the Naval Installation Restoration Information Solution (NIRIS) address environmental considerations during planning and decision making. Contact information is listed below:

Naval Facilities Engineering Command, Mid Atlantic
9742 Maryland Avenue
ATTN CODE OPTE3-2
Norfolk, VA 23511-3095

7.0 REFERENCES

Brown and Root Environmental. October 1996. Community Relations Plan for Portsmouth Naval Shipyard, Kittery, Maine.

Johnston, R. K., W. R. Munns, Jr., F. T. Short, and H. A. Walker, December 1994. Estuarine Ecological Risk Assessment Phase I: Problem Formulation for Portsmouth Naval Shipyard, Kittery, Maine.

Kearney & Baker/TSA, July 1986. RCRA Facility Assessment, Portsmouth Naval Shipyard, A.T. Kearney, Inc., Alexandria, VA and Baker/TSA, Inc., Beaver, Pennsylvania.

LEA, June 1986. Final Confirmation Study Report on Hazardous Waste Sites at Portsmouth Naval Shipyard, Kittery, Maine. Loureiro Engineering Associates, Avon, Connecticut.

Louis Berger Group, April 2003. Cultural Resources Survey, Portsmouth Naval Shipyard, Kittery, Maine. Louis Berger Group, Inc., East Orange, New Jersey.

McLaren/Hart, July 1992. Draft RCRA Facility Investigation Report, Portsmouth Naval Shipyard, Kittery, Maine. McLaren/Hart Environmental Engineering Corporation, Albany, New York.

McLaren/Hart, August 1992. Onshore Ecological Risk Assessment for Portsmouth Naval Shipyard, Kittery, Maine. McLaren/Hart Environmental Engineering Corporation, Albany, New York.

McLaren/Hart, May 1994. Final Human Health Risk Assessment Report for Offshore Media, Portsmouth Naval Shipyard. Addendum to Public Health and Environmental Risk Evaluation Part A (McLaren/Hart, March 1994). McLaren/Hart Environmental Engineering Corporation, Albany, New York.

Navy, May 1999. Interim Record of Decision for Operable Unit 4, Portsmouth Naval Shipyard, Kittery, Maine.

Navy, August 2001. Record of Decision for Operable Unit 3, Portsmouth Naval Shipyard, Kittery, Maine.

Navy, September 2003. Explanation of Significant Difference for the Record of Decision for Operable Unit 3. Portsmouth Naval Shipyard, Kittery, Maine.

Navy, October 2005. Explanation of Significant Difference for the Record of Decision for Operable Unit 3. Portsmouth Naval Shipyard, Kittery, Maine. (Dated September 2005 and signed in October 2005.)

Navy, January 2006. Action Memorandum for Site 30, Portsmouth Naval Shipyard, Kittery, Maine. [Dated January and signed in June 2006.]

Navy, September 2010. Record of Decision for Operable Unit 1. Portsmouth Naval Shipyard, Kittery, Maine.

Navy, July 2010. Draft Feasibility Study Report for Operable Unit 4. Portsmouth Naval Shipyard, Kittery, Maine.

Navy, September 2011. Record of Decision Operable Unit (OU) 2 Site 6,29 and DRMO Impact Area. Portsmouth Naval Shipyard, Kittery, Maine.

NCCOSC (Naval Command, Control, and Ocean Surveillance Center), May 2000. Final Estuarine Ecological Risk Assessment for Portsmouth Naval Shipyard, Kittery, Maine. NCCOSC, Narragansett, Rhode Island.

TRC Companies, May 1993. Final Hazard Ranking System Package for Portsmouth Naval Shipyard, Kittery, Maine (ME7170022019), Revision 2. TRC Companies, Inc., Lowell, Massachusetts.

TtNUS, October 1999. Interim Offshore Monitoring Plan for Operable Unit 4 for Portsmouth Naval Shipyard. TtNUS, King of Prussia, Pennsylvania.

TtNUS, March 2000. Field Investigation Report, Site 10 (Building 238) and Site 29 (Teepee Incinerator), for Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, May 2000. Site Screening Report, Site 30 (Building 184), Site 31 (West Timber Basin), and Site 32 (Topeka Pier), Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania. [Revision pages to March 2000 draft final version were provided in May 2000 to finalize the report.]

TtNUS, May 2000. Revised Operable Unit 3 Risk Assessment Volume 1 and 2 – Text and Appendices A Through I. Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, November 2000. Revised OU2 Risk Assessment, Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, November 2001. Preliminary Remediation Goals for Operable Unit 4, Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, July 2002. Baseline Interim Offshore Monitoring Report for Operable Unit 4, Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania. TtNUS, March 2003. Site 10 Additional Investigation Report for Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, August 2004. Site Screening Investigation Report for Site 34 for Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania. (Includes Site 34 Site Investigation Data Package for Portsmouth Naval Shipyard, Kittery, Maine, TtNUS, King of Prussia, Pennsylvania, December 2003, as Appendix A.)

TtNUS, November 2004. Rounds 1 through 7 Interim Offshore Monitoring Program Report, Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania. [Letter dated January 13, 2005 indicates that November 2004 draft final (Rev 0) is the final document.]

TtNUS, August 2005a. Additional Scrutiny Quality Assurance Project Plan for Operable Unit 4 (OU4) at Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, August 2005b. Engineering Evaluation/Cost Analysis (EE/CA) for Site 30 (Building 184) (Revision 1), Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, September 2005. Engineering Evaluation/Cost Analysis (EE/CA) for Site 34, Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, February 2006. Additional Scrutiny Investigation (for OU4) Data Package, Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, June 2006a. Site 10 Data Gap Investigation Quality Assurance Project Plan, Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, January 2006b. Round 8 Interim Offshore Monitoring Program Data Package, Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, June 2007. Five-Year Review Report, Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, July 2007. Remedial Investigation Report for Operable Unit 1, Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, August 2007. Additional Scrutiny Report for Operable Unit 4, Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, February 2010. Rounds 1 through 10 Interim Offshore Monitoring Program Report for Operable Unit 4, Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, March 2010. Supplemental Remedial Investigation Report for Operable Unit 4, Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, June 2010. Feasibility Study Report for Operable Unit 1. Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, November 2010. Final Interim Offshore Monitoring Plan (Revision 1) for Operable Unit 4 for Portsmouth Naval Shipyard. TtNUS, King of Prussia, Pennsylvania.

TtNUS, April 2011. Final Feasibility Study Report for Operable Unit 2. Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

TtNUS, July 2011. Final Remedial Investigation Report Operable Unit (OU) 7. Portsmouth Naval Shipyard, Kittery, Maine. TtNUS, King of Prussia, Pennsylvania.

USEPA (United States Environmental Protection Agency), March 1989, HSWA Permit for Portsmouth Naval Shipyard, Permit Under the Hazardous and Solid Waste Amendments of 1984. USEPA, March 10.

Weston, June 1983. Initial Assessment Study of Portsmouth Naval Shipyard. Naval Energy and Environmental Support Activity, NEESA 13-032, Port Hueneme.

TABLES

**Table 1
Major Phases of the CERCLA Process
Portsmouth Naval Shipyard, Kittery, ME**

Phase	Description
Preliminary Assessment (PA) / Site Investigation (SI)	<p>The PA is a limited assessment designed to differentiate between sites that may pose a threat to human health or the environment and require further investigation and sites that pose little or no threat. At Federal Facilities, the lead agency (the Navy) collects the data for the PA, and USEPA evaluates the PA data. The PA relies heavily on existing information, and environmental samples are rarely collected. If the PA results in a recommendation for further investigation, an SI is conducted.</p> <p>The SI generally includes collection of environmental and waste samples to determine if activities at the site have impacted environmental media and if a site should be included in the CERCLA RI/FS process. As outlined in the FFA, the Site Screening Process (SSP) is an alternative to the PA/SI process.</p>
Remedial Investigation (RI)	<p>The RI collects environmental samples to determine the nature and extent of contamination, potential migration pathways, toxicity and persistence of contaminants, and potential (risk) for adverse impacts to human health or the environment.</p>
Feasibility Study (FS)	<p>The FS develops remedial objectives, identifies ARARs (Applicable or Relevant and Appropriate Requirements), identifies and screens remedial technologies, develops and analyzes remedial alternatives, and compares the alternatives against the CERCLA criteria (protection of human health and the environment, compliance with ARARs, reduction of toxicity, mobility, or volume through treatment, short-term effectiveness, long-term effectiveness, implementability, cost, state acceptance, community acceptance) in support of selecting a remedy.</p>
Proposed Plan (PP) / Proposed Remedial Action Plan (PRAP)	<p>The PP or PRAP presents the remedial alternatives developed in the FS and describes the preferred remedial alternative recommended for implementation. The public has an opportunity to comment during a formal public comment period.</p>
Treatability Study	<p>Treatability studies are performed to assist in the evaluation of a potentially promising remedial technology. The primary objectives of treatability testing are to provide sufficient data to allow treatment alternatives to be fully developed and evaluated during the FS and support the remedial design of a selected alternative. The need for a treatability study is generally identified during the FS, but treatability studies may be conducted at any time during the CERCLA process. Treatability studies can be bench-scale (laboratory study) and/or pilot-scale (field studies).</p>
Engineering Evaluation/Cost Analysis (EE/CA) and Removal Action	<p>Removal actions are implemented to clean up or remove hazardous substances from the environment to mitigate the spread of contamination. Removal actions may be implemented at any time during the CERCLA process. Actions taken immediately to mitigate an imminent threat to human health or the environment, such as the removal of corroded or leaking drums, are classified as time-critical removal actions. Removal actions that may be delayed for 6 months or more without significant additional harm to human health or the environment are classified as non-time-critical removal actions. The EE/CA identifies the objectives of the removal action and analyzes the effectiveness, implementability, and cost of various alternatives.</p>
Record of Decision (ROD)	<p>The ROD is issued to explain the selected remedial action. Public comments received during the PP are addressed as part of the Responsiveness Summary in the ROD. A notice to the public is issued when the ROD is signed by Navy and USEPA following State concurrence.</p>
Remedial Design (RD) and Remedial Action (RA)	<p>The RD phase develops technical specifications for cleanup remedies and technologies to be designed, and if necessary includes generating the Land Use Control Remedial Design. The RA is the actual construction or implementation phase of the cleanup process.</p>
Five Year Review	<p>Five-year reviews generally are required when hazardous substances remain on site above levels that do not permit unlimited use and unrestricted exposure. Five-year reviews provide an opportunity to evaluate the implementation and performance of a remedy to determine whether it remains protective of human health and the environment.</p>
Response Complete (RC)/Remedy In Place (RIP)	<p>The RIP milestone signifies the completion of the remedial action construction phase and that the remedy has been implemented and has been demonstrated to be functioning as designed. RC is the point at which the remedy has achieved the required reduction in risk to human health and the environment (cleanup goals have been met). RC is followed by site closeout. Once all RCs and RIPs have been documented for every site at the facility and the terms of the FFA have been met, site closeout and NPL deletion is completed.</p>

**Table 2
Summary of Environmental Restoration Program Sites
Portsmouth Naval Shipyard, Kittery, Maine**

Site	Other ID ¹			Operable Unit ²	Site Name ²	Site Description	Current CERCLA Status	Comments/Notes
	IAS (1983)	RFI (1992)	FFA (1999)					
10	Not Identified	SWMU 10	SWMU 10	OU1	Former Battery Acid Tank No. 24	Past release of acidic discharges from piping and former underground storage tank associated with lead-acid battery recharging operations in Building 238 at the site resulted in soil contamination on site and sediment contamination off shore (in a portion of the Dry Dock AOC). Tank and surrounding soil was removed in 1986 as part of tank closure. Soil where unacceptable risks identified excavated and disposed off-site as Remedial Action (2011-2012). LUCs in place will prevent future residential land use.	LTMgt	OU1 RI Report finalized in July 2007. OU1 FS Report and PRAP were finalized in June 2010. OU1 ROD was signed in September 2010. Remedial Action consisting of excavation and backfill performed October 2011 to March 2012. Final LUCRD was filed with the appropriate municipal land use offices in Kittery, ME and Portsmouth, NH in March 2012 to prevent residential use of the property and there will be no further risk exposure. Post-Remediation Groundwater Monitoring results indicated that all lead concentrations in groundwater are less than Project Action Levels, and that no further groundwater sampling is required.
6	Not Identified	SWMU 6	SWMU 6	OU2	Defense Reutilization and Marketing Office (DRMO) Storage Yard including DRMO Impact Area (Quarters S, N, and 68)	Storage area for used materials that previously included lead and nickel-cadmium battery elements. In 1983 open storage of batteries was discontinued. In 1993 portions of site were capped or paved as part of interim corrective measures. In 1999, 2005, 2006, and 2008 shoreline stabilization activities were conducted for different portions of the shoreline. A removal action conducted for the DRMO Impact Area in 2010 consisted of soil excavation and off-site disposal.	RA	OU2 Supplement RI Report finalized in March 2010. OU2 FS Report and PRAP finalized in April and August 2011. OU2 ROD signed in September 2011. Final LUCRD filed with the appropriate municipal land use offices in Kittery, ME and Portsmouth, NH in March 2012. Final Remedial Design submitted in November 2012. Final Remedial Action Work Plans for Waste Disposal Area and DRMO Area submitted Summer 2013. Remedial Action (excavation and off-site disposal) commenced Summer 2013 and was completed in Summer 2014.
29	Not Identified	Part of SWMU 6	Teepee Incinerator		Former Teepee Incinerator Site	Area formerly used for open burning, waste disposal, and industrial incineration. Site 29 was separated from Site 6 and made into a new site in 1998. Shoreline stabilization activities at Site 6 in 2005, 2006, and 2008 included a portion of the Site 29 shoreline.		
8	Site 1	SWMU 8	SWMU 8	OU3	Jamaica Island Landfill (JILF)	Historic 25-acre landfill. OU3 RA completed from 2002 to 2004 and included capping 22 acres and removal of 3 acres and replacement with wetlands.	LTM	OU3 ROD signed in 2001 addressed soil and groundwater. OU3 ESDs (2003 and 2005) for excavation, consolidation, and wetlands construction and to include groundwater migration remedy into OU3. Five-year review reports in 2007 and 2012. OU3 post-remedial OM&M has been performed since 2006. The final LUCRD was filed with the appropriate municipal land use offices in Kittery, ME and Portsmouth, NH in August 2011. Annual LUC and landfill inspections are performed. An updated OM&M Plan was submitted in December 2011. Per agreement between the Navy, EPA, and MEDEP in December 2012, annual landfill gas sampling and groundwater sampling for arsenic was discontinued.
9	Sites 3 and 4	SWMU 9	SWMU 9		Former Mercury Burial Sites (MBI and MBII)	Concrete blocks and pipes containing mercury-contaminated wastes were buried within the Site 8 boundary. These vaults were removed in 1990s. No residual contamination from Site 9 found. Site 9 addressed by OU3 RA (see Site 8).		
11	Not Identified	SWMU 11	SWMU 11		Former Waste Oil Tanks Nos. 6 & 7	Former waste oil tanks within Site 8 boundary stored waste oils prior to offsite disposal. Tanks and soil removal performed in 1989. Site 11 addressed by OU3 RA (see Site 8).		
5	Site 2	SWMU 5	SWMU 5	OU4	Former Industrial Waste Outfalls	Numerous discharge points in the dry dock area were formerly used to discharge liquid industrial waste. Discharges were to the Dry Doc AOC portion of the offshore (see Offshore AOCs).	RA	The Offshore HHRA in 1994 evaluated human health risks to surface water and sediment. The OU4 Interim ROD signed in 1999 established interim offshore monitoring for sediment. The EERA evaluated ecological risks to surface water and sediment. FS and PRAP finalized in September 2012 and February 2013, respectively. ROD for OU4 signed in August 2013. Draft Remedial Action Work Plan submitted in Summer 2014 with Remedial Action (removal and off-site disposal) anticipated to start in 2014.
Offshore AOCs	Not Identified	Not Identified	Offshore Areas		Offshore Areas Potentially Impacted by PNS Onshore IRP Sites	Based on the EERA (2000), six AOCs were identified in the offshore area that could have been impacted by onshore IRP releases. These are the Back Channel, Jamaica Cove, Clark Cove, Sullivan Point, DRMO Storage Yard, and Dry Dock AOCs. The interim offshore monitoring plan (1999), as required by the Interim ROD (1999), identified 14 monitoring stations the cover the offshore AOCs.		

**Table 2
Summary of Environmental Restoration Program Sites
Portsmouth Naval Shipyard, Kittery, Maine**

Site	Other ID ¹			Operable Unit ²	Site Name ²	Site Description	Current CERCLA Status	Comments/Notes
	IAS (1983)	RFI (1992)	FFA (1999)					
32	Not Identified	Not Identified	Topeka Pier Site (SSA)	OU7	Topeka Pier Site	The 17-acre area was formerly used as a timber basin and was filled with soil, debris, and some waste material. Emergency removal action and shoreline stabilization conducted in 2006.	RA	Soil, groundwater, intertidal surface water, and sediment sampling was conducted, and the OU7 RI was finalized in November 2011. The Final FS was submitted in June 2013, and the PRAP was finalized in May 2013. The ROD for OU7 was signed on September 30, 2013. The Final LUCRD will be filed with the appropriate municipal land use offices in Kittery, ME and Portsmouth, NH in 2014. The draft Remedial Action Work Plan for soil excavation will be submitted in Summer 2014, and the excavation and off-site disposal portion of the ROD selected remedy is planned to commence in 2014.
31	Not Identified	Not Identified	West Timber Basin (SSA)	OU8	Former West Timber Basin	Site originally for storage and seasoning wood for ship production, and metal washing and pickling activities occurred at the site. Portions of the site were filled in.	RI	Added as site based on 1998 SSI soil and groundwater sampling results. Draft RI Sampling and Analysis Plan submitted in April 2014, with RI field investigation activities anticipated to start in 2014.
34	Not Identified	Not Identified	Oil Gasification Plant, Building 62 (SSA)	OU9	Former Oil Gasification Plant, Building 62	Site was originally the location of the oil gasification plant. Site also used for blacksmith shop and pesticide storage. Burning of coal as part of operations resulted in contaminated soil around the building. Non-time-critical removal action completed in 2007 included excavation and offsite disposal of the ash pile and ash exposed at shoreline ledge areas. The ash removal action addressed nearly all unacceptable risks at the site.	LUCRD	Soil sampling conducted in 2009 and 2010 to support RI. OU9 RI Report finalized in June 2012. The Final FS was submitted in June 2013, and the PRAP was finalized in July 2013. The ROD for OU9 was signed on September 30, 2013, with Land Use Controls as selected remedy. The Final LUCRD will be filed with the appropriate municipal land use offices in Kittery, ME and Portsmouth, NH in FY 2014.
30	Not Identified	Not Identified	Galvanizing Plant, Building 184 (SSA)	SSA	Former Galvanizing Plant, Building 184	Originally a galvanizing plant where four-foot deep concrete tank vault within building contained pickling tanks and was later used for metal parts assembly. The tank vault was filled in during the 1960s, and fill material has high acid content (i.e., low pH). 2006 and 2007 removal action to remove crystalline material and redirect storm water away from building.	NFA	An EE/CA (Revision 2) was prepared for removal of tank vault contents and tank vault and associated Action Memorandum (Revision 2) was signed in December 2010. Removal action completed September to November 2011 and included removal of remaining equipment and the office that was on top of the floor covering the vault, removal of the concrete floor slab, and removal of the vault fill material. The Final Construction Completion Report was submitted in November 2013. The No Further Action Decision Document was submitted in March 2014.

Notes:

1. Other site identification nomenclature from previous documents.

IAS = Initial Assessment Study, June 1983, Administrative Record Number 000002

RFI = RCRA Facility Investigation Report (draft), July 1992, Administrative Record Number 000117

FFA = Federal Facilities Agreement, September 1999, Administrative Record Number 000726. Site designation in FFA as provided in Appendices B (List of Areas of Concern) and C (List of Site Screening Areas) of the FFA.

2. Operable unit designation and Site Name are based on the Site Management Plan (SMP) provided in Appendix D of the FFA and subsequent annual amendments of the SMP.

**Table 3
Sites Removed from Environmental Restoration Program
Portsmouth Naval Shipyard, Kittery, Maine**

Site	Other ID ¹			Operable Unit	Site Name	Site Description	Current CERCLA Status	Comments/Notes ²
	RFA (1986)	RFI (1992)	FFA (1999)					
1	SWMU 1	NA	NA	NA	Hazardous Waste Storage Facility	This unit was an active container storage area with a RCRA Permit. No additional action was required because it was a licensed RCRA facility with frequent inspections and no history of releases.	NFA	Eliminated from further investigation in the RFA.
2	SWMU 2	NA	NA	NA	Freon Recovery Operation	This unit was a still located in Building 174 and holding tank located outside of Building 174 that were used for reclaiming Freon solvent used in various operations. No additional action was required because the unit was certified closed in accordance with a State approved closure plan.	NFA	Eliminated from further investigation in the RFA.
3	SWMU 3	NA	NA	NA	Industrial Waste Treatment Plant	The treatment plant was located in Building 298. No additional action was required because there was no history of releases and the plant was in the process of obtaining a RCRA Permit.	NFA	Eliminated from further investigation in the RFA.
4	SWMU 4	NA	NA	NA	Interim Storage Facilities	This unit consisted of four temporary waste holding areas that were used before transfer of wastes to the Hazardous Waste Storage Facility (SWMU 1). No additional action was required because the unit was certified closed in accordance with a State approved closure plan.	NFA	Eliminated from further investigation in the RFA.
7	SWMU 7	NA	NA	NA	Interim Storage Areas	This unit consisted of four waste storage areas that were used for the storage of drummed facility wastes. No additional action was required because the unit was certified closed in accordance with a State approved closure plan.	NFA	Eliminated from further investigation in the RFA.
12	SWMU 12	SWMU 12	NA	NA	Boiler Blowdown Tank, Building 72 (Tank No. 25)	This unit was a 3,800-gallon underground, steel tank for boiler blowdown. The tank was removed as part of the RFI. There were no releases from this unit, and subsequently no further action was required.	NFA	NFA Decision Document signed July 1997 (AR No. 000447).
13	SWMU 13	SWMU 13	NA	NA	Rinse Water Tank, Building 76 (Tank No. 27)	This unit was a 700-gallon underground, steel tank for rinse waters from Building 76. The tank was removed as part of the RFI. There were no releases from this unit, and subsequently no further action was required.	NFA	NFA Decision Document signed July 1997 (AR No. 000447).
14	SWMU 14	NA	NA	NA	Waste Oil Tank No. 31	This unit was a 750-gallon underground, steel tank that was used to hold used oil from Building 72.	NFA	Eliminated from further investigation in the RFA.
15	SWMU 15	NA	NA	NA	Oil/Water Separator No. 32	This unit was a 5,400-gallon fiberglass tank used for oily wastewaters from Building 72.	NFA	Eliminated from further investigation in the RFA.
16	SWMU 16	SWMU 16	NA	NA	Rinse Water Tank, Building 174 (Tank No. 34)	This unit was a 750-gallon underground, steel tank that was used to hold rinse waters from Building 174. The tank was removed as part of the RFI. There were no releases from this unit, and subsequently no further action was required.	NFA	NFA Decision Document signed July 1997 (AR No. 000447).
17	SWMU 17	NA	NA	NA	Floor Drain Tank No. 26	It was determined that this unit did not exist.	NFA	Eliminated from further investigation in the RFA.
18	SWMU 18	NA	NA	NA	Waste Lube Tank No. 35	This unit was a 4,500-gallon aboveground, steel tank used for used lubrication oil storage. No further action was required because it was a new tank (installed in 1982).	NFA	Eliminated from further investigation in the RFA.
19	SWMU 19	NA	NA	NA	Waste Oil Tank No. 37	This unit was a 500-gallon underground, steel tank that held used oil. No further action was required because it was a new tank (installed in 1985).	NFA	Eliminated from further investigation in the RFA.
20	SWMU 20	NA	NA	NA	Oil/Water Separator No. 38	This unit was a partially buried oil/water separator. No further action was required because it was a new unit (installed in 1985).	NFA	Eliminated from further investigation in the RFA.
21	SWMU 21	SWMU 21	SWMU 21	OU1	Acid/Alkaline Drain Tank No. 28	This unit was a 695-gallon underground tank that was used to store spent acid/alkaline cleaning solutions. The tank was removed as part of the RFI. Soil and groundwater sampling was conducted to confirm that a release from the tank did not result in unacceptable risks, and subsequently no further action was required.	NFA	NFA Decision Document signed February 2008 removed Site 21 from OU1. (AR No. 001647).

**Table 3
Sites Removed from Environmental Restoration Program
Portsmouth Naval Shipyard, Kittery, Maine**

Site	Other ID ¹			Operable Unit	Site Name	Site Description	Current CERCLA Status	Comments/Notes ²
	RFA (1986)	RFI (1992)	FFA (1999)					
22	SWMU 22	NA	NA	NA	Chemical Cleaning Facility Tank, Building 155	This unit was a 4,000 gallon aboveground tank for collecting spills and wastes from metal surface cleaning operations. No further action was required because there was low potential for release.	NFA	Eliminated from further investigation in the RFA.
23	SWMU 23	SWMU 23	NA	NA	Chemical Cleaning Facility Tank, Building 174	This unit was a 2,270-gallon underground tank used to hold rinse waters from Building 174. The tank was removed as part of the RFI. There were no releases from this unit, and subsequently no further action was required.	NFA	NFA Decision Document signed July 1997 (AR No. 000447).
24	SWMU 24	NA	NA	NA	Asbestos Collection Dumpster	This unit was a central collection dumpster for asbestos waste that was located adjacent to the Hazardous Waste Storage Facility (SWMU 1). No further action was required because there was low potential for release.	NFA	Eliminated from further investigation in the RFA.
25	SWMU 25	NA	NA	NA	Burnable Dumpsters	This unit consisted of dumpsters to collect burnable wastes consisting mostly of paper. No further action was required because there was no evidence of a release of hazardous wastes or constituents.	NFA	Eliminated from further investigation in the RFA.
26	SWMU 26	SWMU 26	SWMU 26	OU4	Portable Oil Water Dumpsters	This unit consisted of dumpsters at the submarine berths used for oil/water wastes from cleanout of submarine bilges and various tanks. No further action was required for this unit because it consisted of portable tanks that were used for petroleum wastes only.	NFA	NFA Decision Document signed August 2001. NFA under CERCLA removed Site 26 from OU4. (AR No. 001019).
27	SWMU 27	SWMU 27	SWMU 27	OU5	Berth 6 Industrial Area/Fuel Oil Spill Area	A ruptured underground pipeline resulted in release of No. 6 fuel oil near Berth 6. The broken pipeline and surrounding contaminated soil was excavated. Other fuel oil lines that ran through Berth 6 that failed hydrostatic testing in 1981 were capped and abandoned in place. It was determined that petroleum product was the only contaminant of concern; therefore, no further action was required.	NFA	NFA Decision Document signed August 2001. NFA under CERCLA removed site from OU5. (AR No. 001020).
28	SWMU 28	NA	NA	NA	Silver Recovery System	Silver recovery operations for wastes with high silver content were conducted in several areas within buildings. Non-recoverable wastes were drummed and stored at the Hazardous Waste Storage Facility (SWMU 1). No further action was required because there was low potential for release.	NFA	Eliminated from further investigation in the RFA.
30	NA	NA	Galvanizing Plant, Building 184 (SSA)	SSA	Former Galvanizing Plant, Building 184	Originally a galvanizing plant where four-foot deep concrete tank vault within building contained pickling tanks and was later used for metal parts assembly. The tank vault was filled in during the 1960s, and fill material had high acid content (i.e., low pH). 2006 and 2007 removal action to remove crystalline material and redirect storm water away from building. Removal Action completed in 2011 with removal of tank vault contents, tank vault, remaining equipment and the office that was on top of the floor covering the vault, removal of the concrete floor slab, and removal of the vault fill material. The No Further Action Decision Document was signed in March 2014.	NFA	NFA Decision Document signed March 2014. (AR No. 002987).
JILF Impact Area	NA	Portion of SWMU 8	JILF Impact Area	OU3	JILF Impact Area (Former CDC)	At the time the RFI for PNS was conducted, the Child Development Center (CDC) was located to the west of the JILF. Sampling in this area was conducted as part of the RFI to ensure that the children at the CDC were not being exposed to soil contaminated by wind dispersal of JILF contamination. When the CDC was moved to a different location, the area was referred to as the Former CDC. The building and playground equipment were removed and the area is currently used as an open-green space, with grass and trees covering the area. Sampling in the area indicated that it had not been impacted by the JILF and no further action was required.	NFA	NFA Decision Document signed in February 2008. NFA removed area from OU3. (AR No. 001648).

Notes:

1. Other site identification nomenclature from previous documents.

IAS = Initial Assessment Study, June 1983, Administrative Record Number 000002

RFA = RCRA Facility Assessment (RFA), July 1986, Administrative Record Number 0000014 (including Addendum to RFA)

RFI = RCRA Facility Investigation Report (draft), July 1992, Administrative Record Number 000117

FFA = Federal Facilities Agreement, September 1999, Administrative Record Number 000726. Site designation in FFA as provided in Appendices B (List of Areas of Concern) and C (List of Site Screening Areas) of the FFA.

AR = Administrative Record

SSA = Site Screening Area

2. SWMUs removed in the RFA were not included in the 1989 HSWA Permit, Administrative Record Number 000019, and no further action was conducted at these SWMUs.

NA - Not applicable because site was not identified in document or not included in an operable unit.

TABLE 4
Summary of Relative Risk Ranking and Remediation Activities Performed
Portsmouth Naval Shipyard, Kittery, Maine


OU	Site	Site Name	Rank	Remediation Performed
1	Site 10	Former Battery Acid Tank No. 24	High	Remedial Action (Soil excavation and disposal) and LUCRD completed in FY 2012. Post-remediation groundwater monitoring concluded that lead was less than Project Action Levels.
	Site 21	Former Acid/Alkaline Drain Tank	Low	No Further Action documented.
2	Site 6	DRMO Storage Yard and Impact Area	High	A portion of the DRMO was capped as an Interim Corrective Measure; Removal Action in 2010 and included shoreline stabilization, excavation, and disposal for DRMO Impact Area. LUCRD completed in FY 2012. Remedial Action completed in FY 2014.
	Site 29	Former Teepee Incinerator Site	High	Shoreline stabilization completed. LUCRD completed in FY 2012. Remedial Action completed in FY 2014.
3	Site 8	JILF and Impact Area	High	Remedial Action completed: cap 22 acres and removal of 3 acres and replacement with wetlands. LUCRD completed in FY 2011. No Further Action required for JILF and Impact Area.
	Site 9	Former Mercury Burial Sites (MBI and MBII)	Low	Vaults removed. Site 9 covered by Site 8 Remedial Action.
	Site 11	Former Waste Oil Tanks Nos. 6 & 7	High	Tanks removed. Site 11 covered by Site 8 Remedial Action.
4	Site 5	Former Industrial Waste Outfalls	High	None. ROD signed in FY 2013. Remedial Action to commence in 2014 to remove contaminated sediment
	Site 26	Portable Oil/Water Tanks	Low	No Further Action documented.
	--	Offshore Areas	High	None. ROD signed in FY 2013. Remedial Action to commence in 2014 to remove contaminated sediment
5	Site 27	Berth 6 Industrial Area	High	No Further Action documented
NA	Site 30	Former Galvanizing Plant, Building 184	High	Removal action completed in Fall 2011 and included removal of the concrete floor slab and the vault fill material. No Further Action Decision Document signed in FY 2014
8	Site 31	Former West Timber Basin	Low	None. Contaminated soils removed as part of construction activities. Remedial Investigation to be performed to evaluate residual contamination.
7	Site 32	Topeka Pier Site	High	None. ROD signed in FY 2013. Remedial Action to Commence in 2014 with excavation to prevent potential current user risk exposure
9	Site 34	Former Oil Gasification Plant, Building 62	High	Removal action performed in 2007 to remove ash to address nearly all unacceptable risks. ROD signed in FY 2013. LUCRD completed in FY 2014

Color Key

No further remediation required	Removal Action performed and/or Remedial Action pending	No remediation performed to date
---------------------------------	---	----------------------------------

Notes: Relative risk ranking was conducted from 1995 to 1999 prior to the signing of the Federal Facilities Agreement.

FIGURES

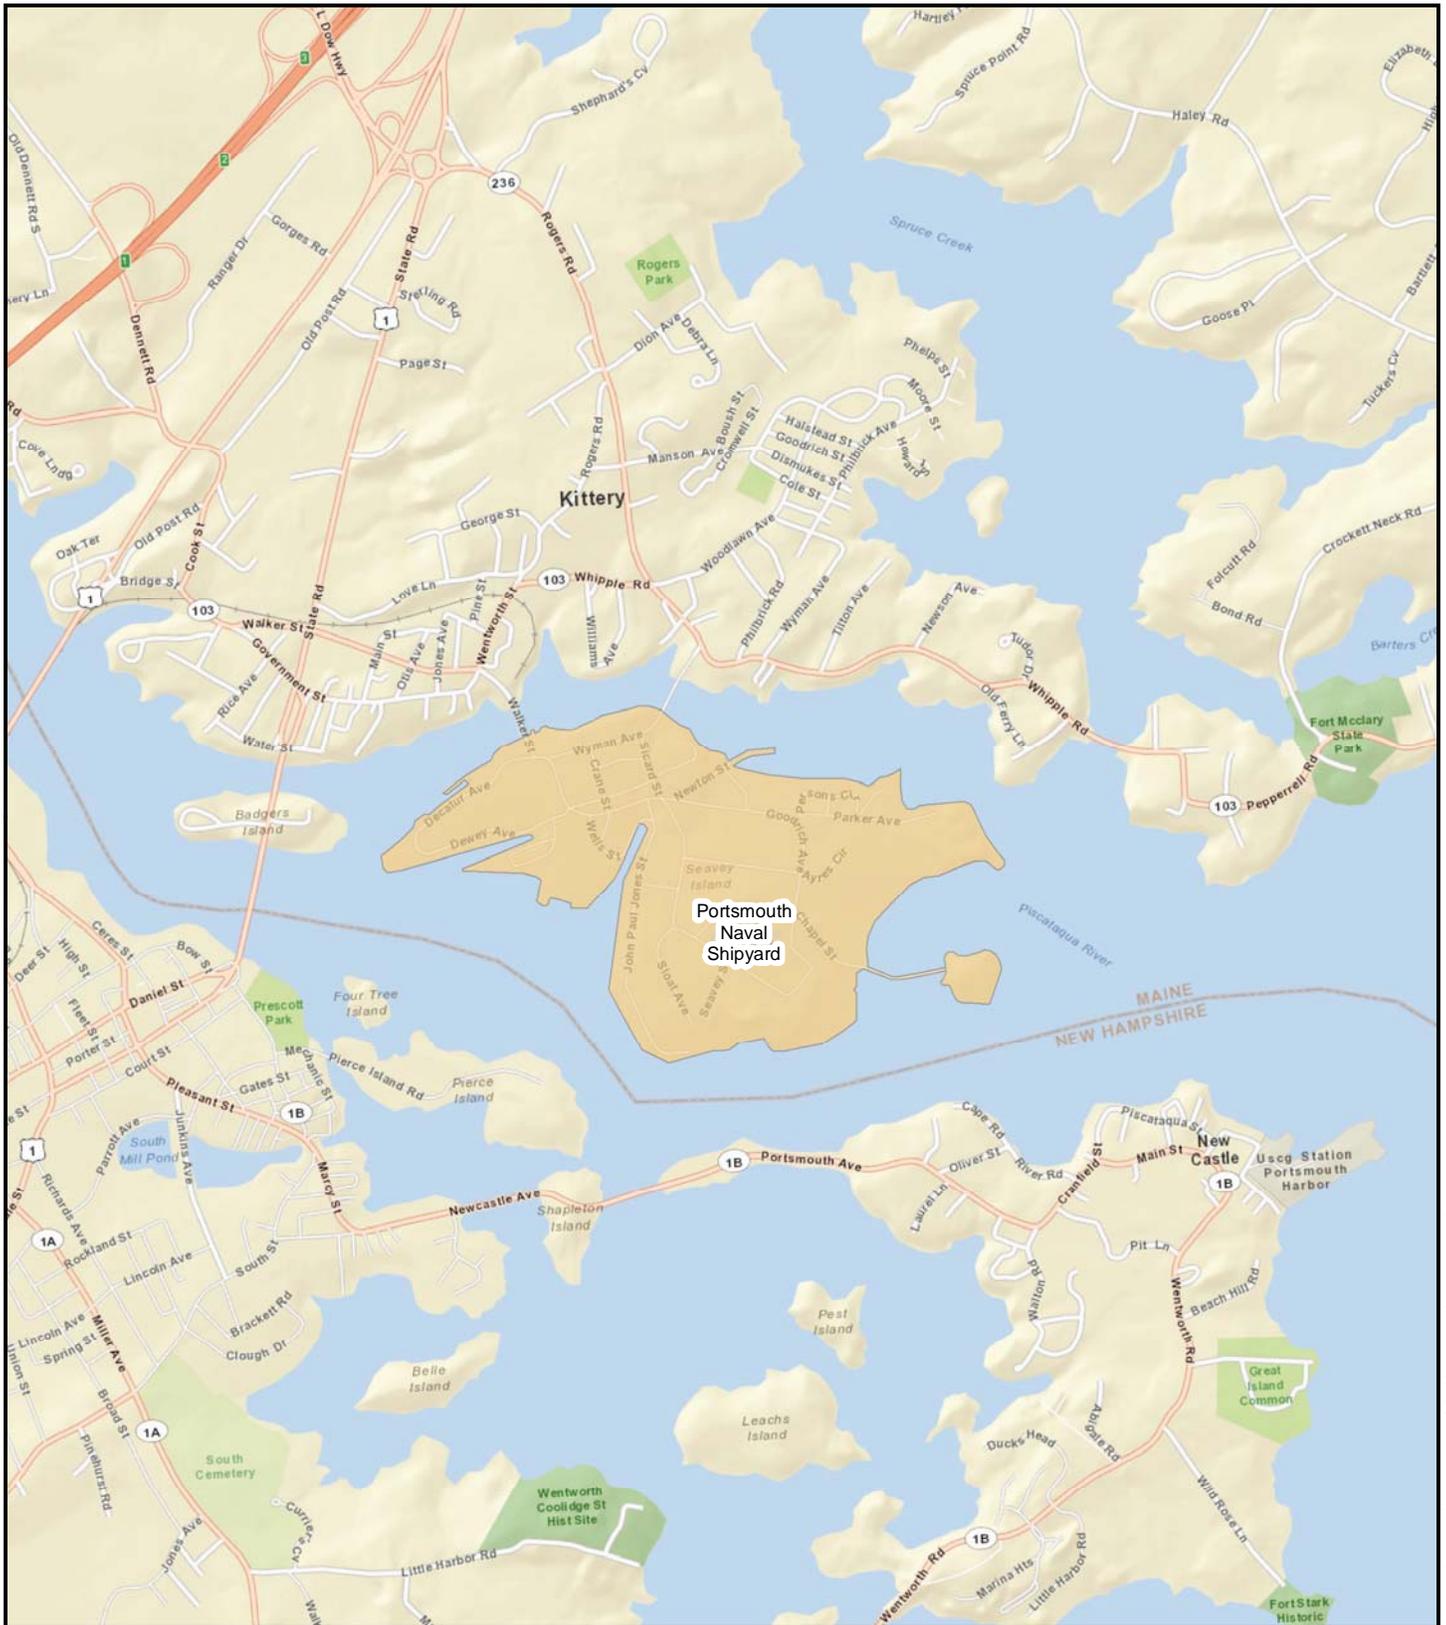

SITE LOCATION MAP
PORTSMOUTH NAVAL SHIPYARD
KITTERY, MAINE

0 500 1,000 2,000 3,000 4,000 5,000 6,000 Feet

0 100 200 400 600 800 1,000 1,200 1,400 1,600 Meters

Scale: 1:24,000




**RESOLUTION
CONSULTANTS**


Figure 1

Date: April 2012

Project #: 60249579

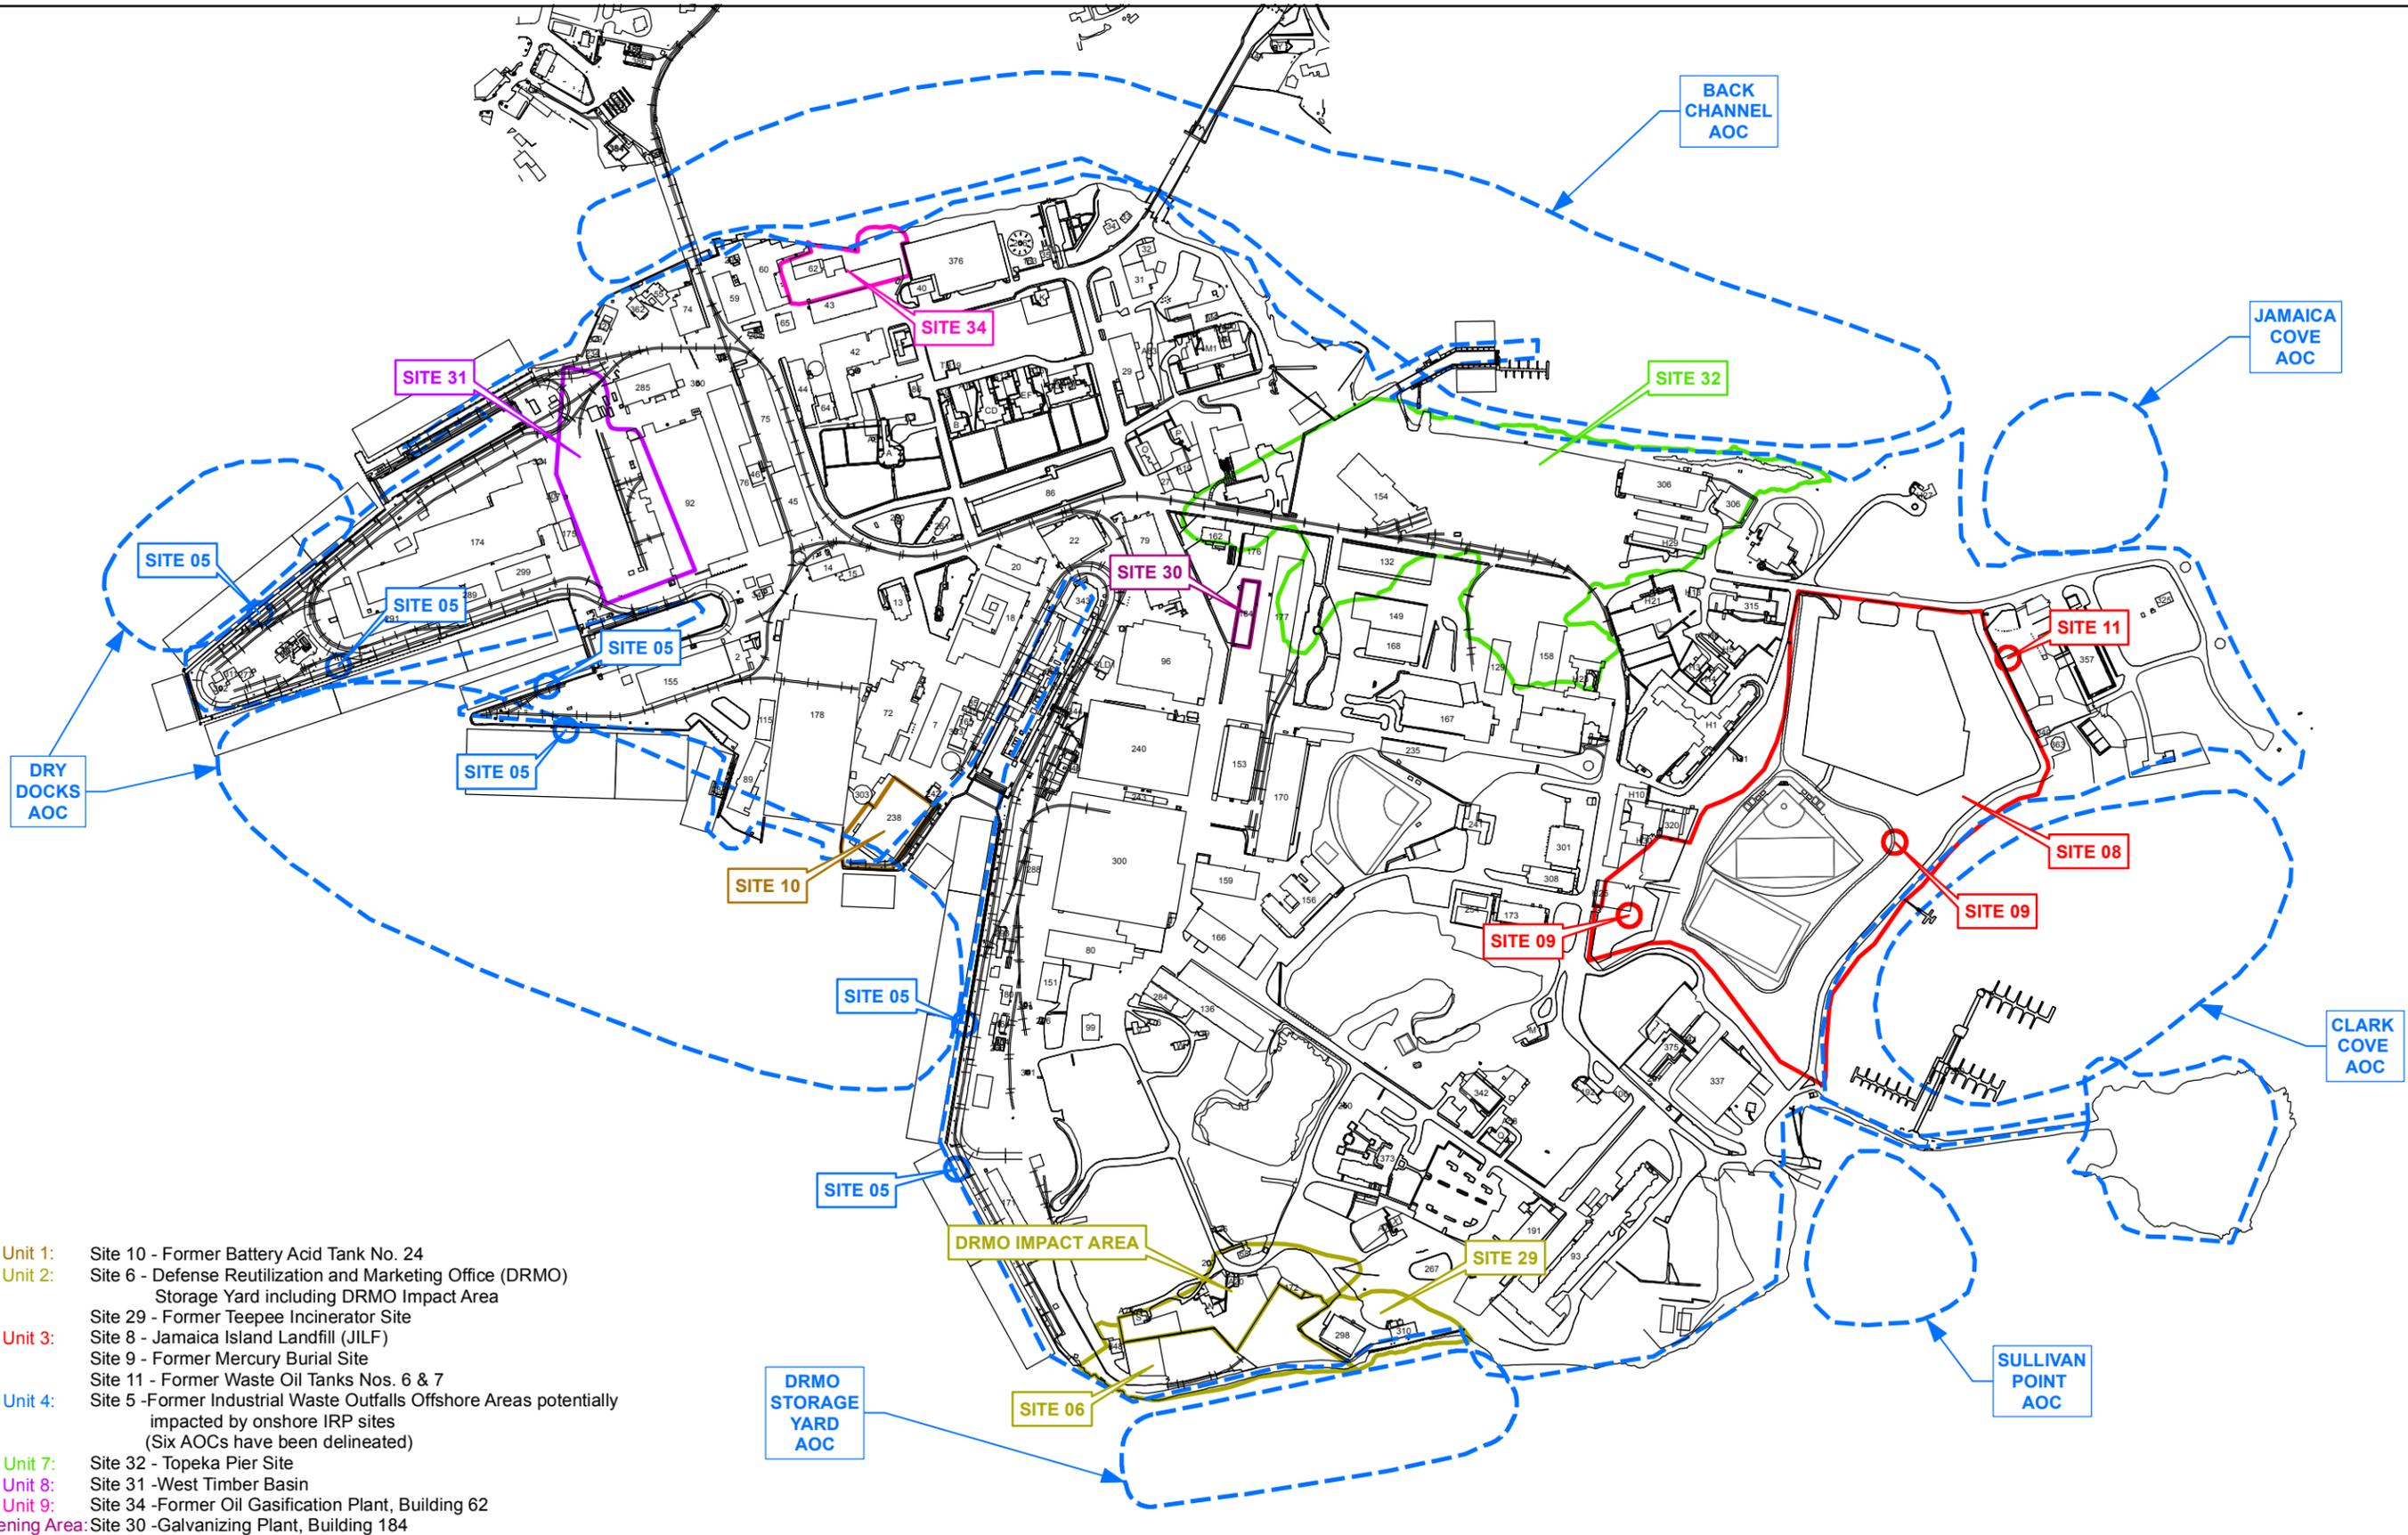


- Operable Unit 1:** Site 10 - Former Battery Acid Tank No. 24
- Operable Unit 2:** Site 6 - Defense Reutilization and Marketing Office (DRMO) Storage Yard including DRMO Impact Area
- Operable Unit 3:** Site 29 - Former Teepee Incinerator Site
Site 8 - Jamaica Island Landfill (JILF)
Site 9 - Former Mercury Burial Site
Site 11 - Former Waste Oil Tanks Nos. 6 & 7
- Operable Unit 4:** Site 5 - Former Industrial Waste Outfalls Offshore Areas potentially impacted by onshore IRP sites
(Six AOCs have been delineated)
- Operable Unit 7:** Site 32 - Topeka Pier Site
- Operable Unit 8:** Site 31 - West Timber Basin
- Operable Unit 9:** Site 34 - Former Oil Gasification Plant, Building 62
- Site Screening Area:** Site 30 - Galvanizing Plant, Building 184



PORTSMOUTH NAVAL SHIPYARD KITTERY, MAINE 60249579		FACILITY PLAN VIEW
DATE: 09/14/12	DRWN: J.E.B.	FIGURE 2

W:\Govt\Projects\Navy\CLEAN AECOM-EnSafe JV\Portsmouth\GIS\Projects\Figure_3_Portsmouth_Naval_Shipyard_Facility_Aerial_View_Map.mxd

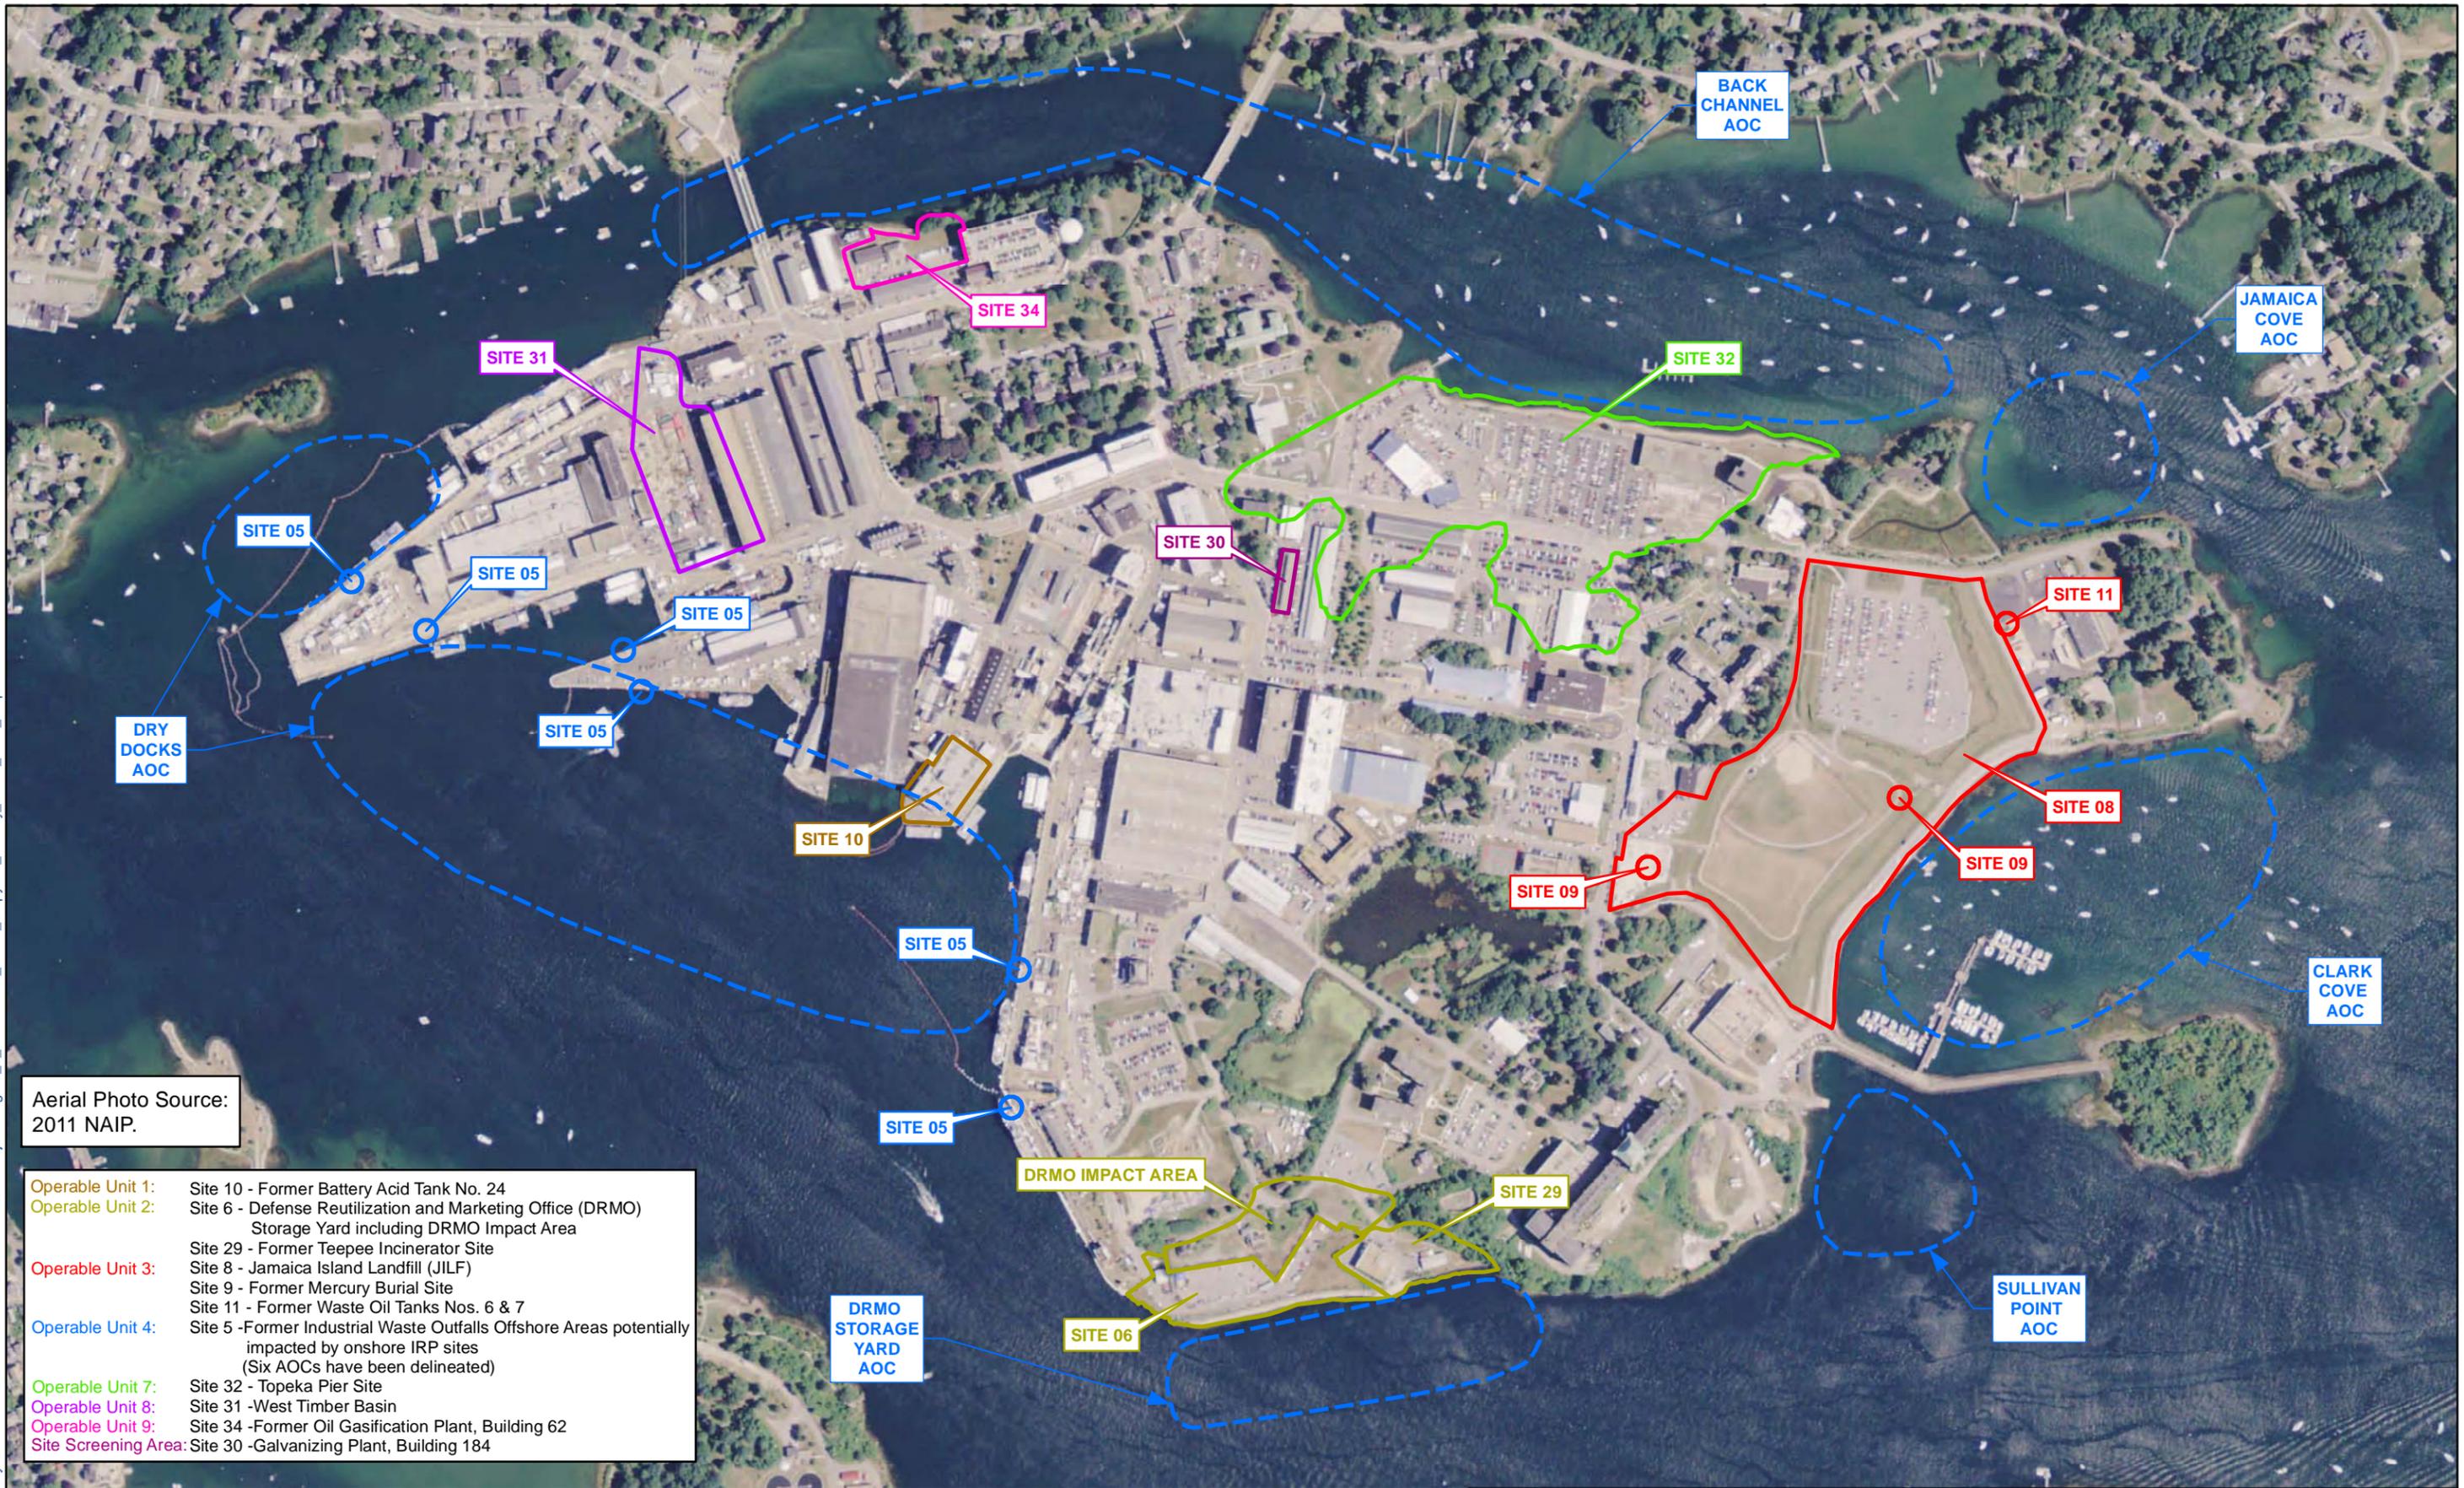

Aerial Photo Source:
2011 NAIP.

- Operable Unit 1:** Site 10 - Former Battery Acid Tank No. 24
- Operable Unit 2:** Site 6 - Defense Reutilization and Marketing Office (DRMO) Storage Yard including DRMO Impact Area
- Operable Unit 3:** Site 29 - Former Teepee Incinerator Site
Site 8 - Jamaica Island Landfill (JILF)
Site 9 - Former Mercury Burial Site
Site 11 - Former Waste Oil Tanks Nos. 6 & 7
- Operable Unit 4:** Site 5 - Former Industrial Waste Outfalls Offshore Areas potentially impacted by onshore IRP sites
(Six AOCs have been delineated)
- Operable Unit 7:** Site 32 - Topeka Pier Site
- Operable Unit 8:** Site 31 - West Timber Basin
- Operable Unit 9:** Site 34 - Former Oil Gasification Plant, Building 62
- Site Screening Area:** Site 30 - Galvanizing Plant, Building 184



PORTSMOUTH NAVAL SHIPYARD KITTERY, MAINE 60249579		FACILITY AERIAL VIEW
DATE: 09/14/12	DRWN: J.E.B.	FIGURE 3



PORTSMOUTH NAVAL SHIPYARD
KITTERY, MAINE
60249579

PORTSMOUTH NAVAL SHIPYARD
FACILITY BIRD'S EYE VIEW

DATE: 04/10/12

DRWN: J.E.B.

FIGURE 4

W:\Govt\Projects\Navy\CLEAN AECOM-EnSafe JV\Portsmouth\GIS\Projects\Figure_5_Portsmouth_Naval_Shipyard_Interim_Offshore_Monitoring_Station_Locations.mxd



Aerial Photo Source:
2011 NAIP.



PORTSMOUTH NAVAL SHIPYARD KITTERY, MAINE 60249579		INTERIM OFFSHORE MONITORING STATION LOCATIONS	
DATE: 04/13/12	DRWN: J.E.B.		FIGURE 5

Attachment A

List of ERP Documents for the Portsmouth Naval Shipyard

ATTACHMENT A

LIST OF ERP DOCUMENTS FOR THE PORTSMOUTH NAVAL SHIPYARD

DOCUMENTS COMPLETED BEFORE SIGNATURE OF FFA

The following documents were completed prior to the FFA being signed in September 1999:

<u>Document</u>	<u>Date</u>	<u>Administrative Record Number</u>
Initial Assessment Study	June 1983	000002
Final Confirmation Study Report on Hazardous Waste Sites	May 1986	000012/000013
RCRA Facility Assessment	July 1986	000014
RCRA Facility Investigation (RFI) Proposal	August 1989	000023
Addendum to RCRA Facility Investigation Proposal	February 1991	000044
Interim Human Health Risk Assessment for Quarters S, N, and 68	April 1991	000052
RCRA Facility Investigation Work Plan	August 1991	000070
Work/Quality Assurance Project Plan for the Case Study for Estuarine Ecological Risk Assessment	September 1991	000072
Interim Human Health Risk Assessment for the Day Care Center	October 1991	000076
Revised Ambient Air Quality Monitoring Report (Section 11 of the RFI)	April 1992	000117
Draft RCRA Facility Investigation Report	July 1992	000117 to 000122
Onshore Ecological Risk Assessment	August 1992	000125
Interim Corrective Measures at the Defense Reutilization and Marketing Office	April 1993	000154
Final Hazard Ranking System Package	May 1993	000162
Addendum to RCRA Facility Investigation Report	June 1993	000169
Background Soil Sampling Work Plan	August 1993	000180
Work/Quality Assurance Plan for Phase II of Estuarine Ecological Risk Assessment Case Study	February 1994	000206
Public Health and Environmental Risk Evaluation Part A: Human Health Risk Assessment Report	March 1994	000211
Final Media Protection Standards Proposal for Onshore Media (Chapter 1)	April 1994	000216
Final Human Health Risk Assessment Report for Offshore Media	May 1994	000229

<u>Document</u>	<u>Date</u>	<u>Administrative Record Number</u>
Media Protection Standards for Offshore Media: Sediment and Surface Water (Chapter 3)	June 1994	000237
RFI Data Gap Work Plan	June 1994	000234
Work Plan for Phase II Ambient Air Quality and Meteorological Monitoring Program	July 1994	000238
Draft Revised Corrective Measures Study Proposal	July 1994	000239
Draft Applicable or Relevant and Appropriate Requirements (ARARs) Report	September 1994	000250
Estuarine Ecological Risk Assessment Phase I: Problem Formulation	December 1994	000261
Draft Onshore Feasibility Study (FS) Report	March 1995	000275
Draft Final Estuarine Ecological Risk Assessment (included in FFA, finalized May 2000)	July 1995	000428
RCRA Facility Investigation (RFI) Data Gap Report	November 1995	000328
Media Protection Standards for Offshore Media Based on Human Health Risks (Chapter 2)	April 1996	000344
Phase II Ambient Air Quality and Meteorological Monitoring Report	June 1996	000356
Community Relations Plan	October 1996	000384
Consensus Document, No Further Action for Soils, SWMU 21	October 1996	000383
Technical Memorandum on Seep Sampling	November 1996	000396
Groundwater Investigation and Monitoring Plan (formerly titled Interim Groundwater Monitoring Plan)	November 1996	000395
Onshore/Offshore Contaminant Fate and Transport Modeling Phase I Work Plan	December 1996	000403
Draft Onshore/Offshore Contaminant Fate and Transport Modeling Phase I Report	February 1997	000419
Technical Memorandum on Risk Evaluation of Surface Soils from Jamaica Island Landfill (JILF) Site	May 1997	000432
Engineering Evaluation/Cost Analysis (EE/CA) for Mercury Burial Site I	June 1997	000441
Decision Document, No Further Action, SWMUs 12, 13, 16, and 23	July 1997	000447
Final Action Memorandum for Mercury Burial Site I	September 1997	000471
MEDEP Evaluation of Heavy Metal Migration at Portsmouth Naval Shipyard with Geochemical Modeling	December 1997	000508

<u>Document</u>	<u>Date</u>	<u>Administrative Record Number</u>
Onshore/Offshore Contaminant Fate and Transport Modeling Phase I Report Addendum	December 1997	000497
Work Plan, Teepee Incinerator (Site 29) and Building 238 (Site 10)	March 1998	000532
Site Screening Process Plan	March 1998	000531
Site Screening Work Plan, Building 184 (Site 30), West Timber Basin (Site 31), and Topeka Pier (Site 32)	April 1998	000546
Final Work Plan for MTADS Geophysical Mapping	September 1998	000598
Onshore/Offshore Contaminant Fate and Transport Modeling Phase II Work Plan	August 1998	000574
Phase I/Phase II Offshore Data Comparative Analysis Report	October 1998	000606
Proposed Plan for Interim Action at OU4	October 1998	000603
Interim Record of Decision for OU4	May 1999	000676
Technical Memorandum Lead Contamination at DRMO Impact Area (finalized February 2000)	July 1999	000699
Groundwater Monitoring Summary Report	August 1999	000714
Proposal for Evaluation of Seep/Sediment Data	September 1999	000884

DOCUMENTS COMPLETED AFTER SIGNATURE OF FFA

The following documents were completed from October 1999 (after the FFA was signed) to June 2014:

<u>Document</u>	<u>Date</u>	<u>Administrative Record Number</u>
Interim Offshore Monitoring Plan for OU4	October 1999	000750
Removal Action Work Plan for DRMO Shoreline Stabilization	October 1999	000749
Onshore/Offshore Contaminant Fate and Transport Phase II Modeling Report	December 1999	000760
Technical Memorandum for Recommended Human Health Risk Assessment Protocol for OU2	December 1999	000924
Technical Memorandum, Lead Contamination at DRMO Impact Area	February 2000	000795
Final Work Plan for Mercury Burial Vault II and Drum Investigation	February 2000	000797
Field Investigation Report, Site 10 (Building 238) and Site 29	March 2000	000811

<u>Document</u>	<u>Date</u>	<u>Administrative Record Number</u>
(Teepee Incinerator)		
Site Screening Report, Site 30 (Building 184), Site 31 (West Timber Basin), and Site 32 (Topeka Pier)	May 2000	000812
Facility Background Development	May 2000	000836
Revised OU3 Risk Assessment	May 2000	000835
Final Estuarine Ecological Risk Assessment	May 2000	000838
Seep/Sediment Summary Report for Data Collected Between December 1996 and November 1997	August 2000	000884
Test Pitting Investigation Report , Jamaica Island Landfill	October 2000	000909
Revised OU2 Risk Assessment	November 2000	000923/000924
Feasibility Study Report for OU3	November 2000	000922
Proposed Remedial Action Plan for OU3	January 2001	000945
Work Plan for Building 184 Subfloor Investigation	February 2001	000968
Final Action Memorandum for Site 6, Defense reutilization and Marketing Office (DRMO) Shoreline Stabilization	June 2001	000995
Final Drum Removal Report for Drum Investigation	June 2001	000999
Final Closeout Report for Mercury Burial Vault Site I	June 2001	001002
Final Removal Action Report for Mercury Burial Vault Site II	June 2001	001003
OU3 Pre-design Investigation Quality Assurance Project Plan	August 2001	001016
Record of Decision for OU3	August 2001	001018
Decision Document for Site 26	August 2001	001019
Decision Document for Site 27	August 2001	001020
Site 10 Additional Investigation Quality Assurance Project Plan	October 2001	001048
Preliminary Remediation Goals for OU4	November 2001	001062
Final MTADS Geophysical Survey (of JILF and Topeka Pier)	December 2001	001074
Test Pitting Investigation Report, Building 184, Site 30	May 2002	001128
OU3 Phase I Remedial Design (specifications and plans)	June 2002	001139
Technical Memorandum, OU3, Evaluation of MBII Waste Consolidation and Jamaica Cove Options	June 2002	001143
Remedial Design Work Plan, Jamaica Island Landfill Phase I Waste Consolidation	June 2002	001149
Baseline Interim Offshore Monitoring Report for OU4	July 2002	001150
Phase II, OU3 Remedial Design Analysis Report (including drawings and specifications)	November 2002	001195

<u>Document</u>	<u>Date</u>	<u>Administrative Record Number</u>
Engineering Evaluation/Cost Analysis (EE/CA), Site 30 (Building 184)	December 2002	001208
Final Remedial Design Work Plan for Jamaica Island Landfill Phase II Cap Construction	January 2003	001226
Site 10 Additional Investigation Report	March 2003	001243
Site 32 Remedial Investigation Quality Assurance Project Plan	March 2003	001239
Site 34 Site Investigation Quality Assurance Project Plan	March 2003	001238
Addendum to Site 32 Remedial Investigation Quality Assurance Project Plan	August 2003	001252
Explanation of Significant Difference for the Record of Decision for OU3	September 2003	001293
Former CDC Area Investigation Report	April 2004	001350
Technical Memorandum, Recommendation regarding Phase II of the Remedial Investigation for Site 32	June 2004	001376
Site Screening Investigation Report for Site 34	August 2004	001389
OU2 Soil Sampling and Treatability Study Work Plan	November 2004	001414
Rounds 1 through 7 Interim Offshore Monitoring Report for OU4	November 2004	001416/001417
Additional Scrutiny Quality Assurance Project Plan for OU4	August 2005	001484
Engineering Evaluation/Cost Analysis (EE/CA) for Site 30 (Building 184) (Revision 1)	August 2005	001485
Engineering Evaluation/Cost Analysis (EE/CA) for Site 34	September 2005	001495
Explanation of Significant Difference for the Record of Decision for OU3	October 2005	001493
Time Critical Removal Action Work Plan for DRMO (Site 29) Shoreline Stabilization	October 2005	001506
OU2 Screening-Level Soil Washing Treatability Study Report	January 2006	001524
Action Memorandum for Non-Time-Critical Removal Action for Site 30	January 2006	001522
Action Memorandum for Non-Time-Critical Removal Action for Site 34	February 2006	001532
Work Plan for Site 29 Removal of Waste Debris and Site 32 Shoreline Stabilization	April 2006	001553
OU3 Remedial Action Report (for the Jamaica Island Landfill Phase I Waste Consolidation and Phase II Cap Construction)	May 2006	001561
Site 10 Data Gap Investigation Quality Assurance Project Plan	June 2006	001564
Post-Remedial Operation, Maintenance and Monitoring Plan for	June 2006	001566/001567

<u>Document</u>	<u>Date</u>	<u>Administrative Record Number</u>
OU3		
Five-Year Review Report for Portsmouth Naval Shipyard	June 2007	001601
Remedial Investigation Report for OU1	July 2007	001606
Additional Scrutiny Report for OU4	August 2007	001612
Phase II Additional Scrutiny Quality Assurance Project Plan	September 2007	001619
OU2 Additional Investigation Quality Assurance Project Plan	October 2007	001626
No Further Action Decision Document for Site 21 – Former Acid/Alkaline Drain Tank	February 2008	001647
No Further Action Decision Document for the Jamaica Island Landfill Impact Area	February 2008	001648
Closeout Report for Site 29 Removal of Waste Debris and Site 32 Shoreline Stabilization	June 2008	001665
Closeout Report for Site 29 Removal Action Stabilization	July 2008	001670
Contractor Closeout Report and As-built Drawings for Site 34 Shoreline Stabilization and Removal Action	July 2008	001670
Site 32 Remedial Investigation Quality Assurance Project Plan, Revision 1	November 2008	001690
Rounds 1 through 4 Data Evaluation Report for OU3 Post-Remedial Operation, Maintenance, and Monitoring Program	July 2009	000910
Sampling and Analysis Plan for OU9 RI	July 2009	001744
Action Memorandum for Non-Time-Critical Removal Action for OU2 DRMO Impact Area	November 2009	001351
Rounds 1 through 10 Interim Offshore Monitoring Report for OU4	February 2010	001716
Supplemental Remedial Investigation Report for OU2	March 2010	001743
Work Plan for Interim Removal Action for OU2 DRMO Impact Area	May 2010	001746
Feasibility Study Report for OU1	June 2010	001754
Proposed Remedial Action Plan for OU1	June 2010	001759
Record of Decision for OU1	September 2010	002495
Engineering Evaluation/Cost Analysis for Site 30, Revision 2	October 2010	002503
Sampling and Analysis Plan for OU2 Pre Design Investigation	November 2010	002513
Interim Offshore Monitoring Plan for OU4, Revision 1	November 2010	002514
Action Memorandum for Non-Time Critical Removal Action for Site 30, Revision 2	December 2010	002518
Remedial Investigation Supplemental Data Package for Operable Unit 9 (OU 9)	January 2011	002556

<u>Document</u>	<u>Date</u>	<u>Administrative Record Number</u>
Health and Safety Plan for Operable Unit 3 (OU 3) Post Remedial Operation, Maintenance and Monitoring Program	January 2011	002605
Final Amended Site Management Plan for Fiscal Year 2011	February 2011	002555
Marine Safety Plan Offshore Sampling at Operable Unit 4 (OU 4)	April 2011	002548
Health and Safety Plan for Offshore Sampling at Operable Unit 4 (OU 4)	April 2011	002547
Final Feasibility Study Report for Operable Unit 2 (OU 2)	April 2011	002554
Rounds 1 Through 9 Data Evaluation Report for Operable Unit 3 (OU 3) Post Remedial Operation, Maintenance and Monitoring Program	April 2011	002563
Pre-Design Investigation Data Package for Operable Unit 2 (OU 2)	July 2011	002557
Final Remedial Investigation Report Operable Unit (OU) 7	July 2011	002634
Round Ten Data Package for Post Remedial Operations, Maintenance and Monitoring Program Operable Unit (OU) 3	July 2011	002637
Final Removal Action Work Plan For Interim Removal Action at Site 30 Former Galvanizing Tank Vault	July 2011	002559
Final Proposed Plan for Operable Unit 2 (OU 2)	July 2011	001689
Land Use Control Remedial Design for Operable Unit 3 (OU 3)	August 2011	002574
Record of Decision Operable Unit (OU) 2 Site 6, 29, and DRMO Impact Area	September 2011	002620
Interim Offshore Monitoring Program Round 11 Data Package for Operable Unit 4 (OU 4)	September 2011	002576
Final Remedial Action Work Plan for Lead Contaminated Soil Removal Operable Unit (OU) 1 Site 10 Building 238	October 2011	002627
Land Use Control Remedial Design Operable Unit (OU) 1	November 2011	002623
Post Remedial Operation, Maintenance, and Monitoring Plan Operable Unit (OU) 3 Volume 1	December 2011	002638
Post Remedial Operation, Maintenance, and Monitoring Plan Operable Unit (OU) 3 Volume 2	December 2011	002639
Sampling and Analysis Plan for Post Remediation Groundwater Monitoring Operable Unit 1 (OU1)	January 2012	002648
Final Remedial Design for Land Use Controls Operable Unit 1 (OU1)	January 2012	002658

<u>Document</u>	<u>Date</u>	<u>Administrative Record Number</u>
Accident Prevention Plan and Site Safety and Health Plan for Post Remediation Groundwater Monitoring Operable Unit 1 (OU1)	January 2012	002647
Remedial Action Design (30% Submission) for Operable Unit 2 (OU 2)	January 2012	002645
Land Use Control Remedial Design for Operable Unit 1 (OU 1)	January 2012	002643
Final Amended Site Management Plan for Fiscal Year 2012	February 2012	002669
Final Land Use Control Remedial Design Operable Unit 2 (OU2)	March 2012	002673
Second Five-Year Review Report for Portsmouth Naval Shipyard	May 2012	002697
Final Remedial Investigation Report for Operable Unit 9 (OU 9)	June 2012	002700
Final Community Involvement Plan Update	June 2012	002714
Final Round 1 Package for Post Remediation Groundwater Monitoring Operable Unit 1 (OU1)	August 2012	002764
Final Round 11 Data Package for Post Remedial OM&M Program for Operable Unit 3 (OU 3)	September 2012	002752
Final Feasibility Study Report for Operable Unit 4 (OU 4)	September 2012	002749
Final Remedial Design for Operable Unit 2 (OU2)	November 2012	002775
Final Construction Completion Report for DRMO Impact Area	December 2012	Not Yet Assigned
Final Proposed Remedial Action Plan for Operable Unit 4 (OU 4)	February 2013	002791
Final Amended Site Management Plan for Fiscal Year 2013	April 2013	002813
Final Feasibility Study Report for Operable Unit 9 (OU 9)	May 2013	002840
Final Feasibility Study Report for Operable Unit 7 (OU 7)	June 2013	002842
Proposed Plan for Operable Unit 7 (OU 7)	July 2013	002851
Proposed Plan for Operable Unit 9 (OU 9)	July 2013	002863
Final Post-Remediation Groundwater Monitoring Report for Operable Unit 1 (OU 1)	July 2013	002864
Final Remedial Action Work Plan for Remedial Action at Operable Unit 2 (OU 2) Defense Reutilization and Marketing Office Area	July 2013	002946
Final Memorandum for Operable Unit 4 (OU 4) Solid Waste Management Unit 5 (SWMU 5) Results for Confirmation Soil Sampling Within Building 178 Intertidal Area	July 2013	002884
Final Remedial Action Work Plan, Waste Disposal Area of Operable Unit 2 (OU 2)	August 2013	Not Yet Assigned
Final Remedial Action Work Plan, DRMO Area of Operable Unit 2 (OU 2)	July 2013	002946
Final Record of Decision for Operable Unit 4 (OU 4) Site 5 and Offshore Areas Potentially Impacted by PNS Onshore Installation Restoration	August 2013	002897

<u>Document</u>	<u>Date</u>	<u>Administrative Record Number</u>
Program Sites		
Technical Memorandum For Discontinuing Annual Groundwater Monitoring at Operable Unit 3 (OU 3) Post Remedial Operation, Maintenance and Monitoring Program	August 2013	002930
Accident Prevention Plan For Pre-Removal Sediment Confirmation Sampling For Operable Unit 4 (OU 4)	September 2013	002923
Final Sampling and Analysis Plan for Pre-Removal Sediment Confirmation Sampling For Operable Unit 4 (OU 4)	September 2013	002924
Record of Decision for Operable Unit 7 (OU 7) Site 32 Topeka Pier Site	September 2013	002925
Record of Decision for Operable Unit 9 (OU 9) Site 34 Former Oil Gasification Plant Building 62	September 2013	002926
Final Construction Completion Report for Remedial Action at Operable Unit 1 (OU 1) Site 10 Building 238	September 2013	002945
Final Technical Memorandum for 2013 Land Use Control Inspection for Operable Unit 1 (OU 1) Solid Waste Management Unit 10 (SWMU 10)	October 2013	002932
Final Technical Memorandum for 2013 Land Use Control Inspection for Operable Unit 2 (OU 2) Solid Waste Management Unit 6 (SWMU 6) and Site 29	October 2013	002933
Final Construction Completion Report for Site 30 Former Galvanizing Tank Vault	November 2013	002939
Draft Land Use Control Remedial Design Operable Unit 7 (OU 7)	December 2013	Draft Document
Land Use Control Remedial Design Operable Unit 9 (OU 9)	December 2013	Draft Document
Final Amended Site Management Plan for Fiscal Year 2014	February 2014	Not Yet Assigned
Final No Further Action Decision Document For Site 30	March 2014	002987
Memorandum Regarding the Re-Evaluation of Facility Background Report	April 2014	002972
Final Work Plan for Groundwater Monitoring Well Abandonment Activities	April 2014	002990
Draft Final Round 12 Data Package for Post Remedial OM&M Program for Operable Unit 3 (OU 3)	April 2014	Draft Document
Draft RI Sampling and Analysis Plan for Operable Unit 8 (OU 8)	April 2014	Draft Document
Draft Pre-Removal Confirmation Sediment Sampling Report for Operable Unit 4 (OU 4)	April 2014	Draft Document
Draft Remedial Action Completion Report for Operable Unit 1 (OU 1)	June 2014	Draft Document
Draft Land Use Control Remedial Design Revision for Operable Unit 1 (OU 1)	June 2014	Draft Document
Draft Remedial Action Work Plan for Operable Unit 4 (OU 4)	June 2014	Draft Document

<u>Document</u>	<u>Date</u>	<u>Administrative Record Number</u>
Final Gas Monitoring Probe Abandonment Plan for Operable Unit 3 (OU 3)	June 2014	Not Yet Assigned

Attachment B

Schedules

PORTSMOUTH NAVAL SHIPYARD
SITE MANAGEMENT PLAN SCHEDULE
OPERABLE UNIT 1 (OU1)
(SITE 10)

Task Name	Start	Finish	2014				2015				2016			
			Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
REMEDIAL ACTION	Thu 11/3/11	Fri 3/16/12												
POST REMEDIATION GROUNDWATER MONITORING REPORT	Fri 1/18/13	Wed 7/10/13												
Prepare Draft Post Remediation Groundwater Monitoring Report	Fri 1/18/13	Fri 3/15/13												
Submit Draft Post Remediation Groundwater Monitoring Report	Mon 3/18/13	Mon 3/18/13												
USEPA & MEDEP Review	Mon 3/18/13	Tue 5/7/13												
Receive Comments on Draft Post Remediation Groundwater Monitoring Report	Fri 5/3/13	Tue 5/7/13												
Comment Resolution	Wed 5/8/13	Fri 6/28/13												
Prepare Final Groundwater Monitoring Report	Wed 5/8/13	Tue 7/9/13												
Submit Final Groundwater Monitoring Report	Wed 7/10/13	Wed 7/10/13												
CONSTRUCTION COMPLETION REPORT (CCR)	Tue 2/21/12	Mon 9/30/13	9/30											
Prepare Draft CCR	Tue 2/21/12	Wed 3/6/13												
Submit Draft CCR	Thu 3/7/13	Thu 3/7/13												
USEPA & MEDEP Review Draft CCR	Thu 3/7/13	Fri 5/10/13												
Receive Regulator Comments on Draft CCR	Tue 5/7/13	Fri 5/10/13												
Comment Resolution	Fri 5/10/13	Fri 9/13/13	13											
Prepare Final CCR	Mon 9/16/13	Mon 9/30/13	9/30											
Submit Final CCR	Mon 9/30/13	Mon 9/30/13	9/30											
REMEDIAL ACTION CLOSEOUT REPORT (RACR)	Fri 2/28/14	Mon 1/5/15												
Prepare Draft RACR	Fri 2/28/14	Fri 6/6/14												
Submit Draft RACR	Fri 6/6/14	Fri 6/6/14												
USEPA & MEDEP Review Draft RACR	Fri 6/6/14	Mon 7/21/14												
Receive Regulator Comments on Draft RACR	Mon 7/21/14	Mon 7/21/14												
Comment Resolution	Mon 7/21/14	Sat 10/4/14												
Prepare Draft Final RACR	Sat 10/4/14	Mon 11/3/14												
Submit Draft Final RACR	Mon 11/3/14	Mon 11/3/14												
USEPA & MEDEP Review Draft Final RACR	Mon 11/3/14	Tue 12/2/14												
Receive Regulator Comments on Draft Final RACR	Tue 12/2/14	Tue 12/2/14												
Prepare Final RACR	Tue 12/2/14	Mon 1/5/15												
Submit Final RACR	Mon 1/5/15	Mon 1/5/15												
LUC INSPECTION	Mon 6/3/13	Mon 6/6/16												
Conduct LUC Inspection - 2013	Mon 6/3/13	Mon 6/3/13												
Conduct LUC Inspection - 2014	Tue 5/13/14	Tue 5/13/14												
Conduct LUC Inspection - 2015	Mon 6/1/15	Mon 6/1/15												
Conduct LUC Inspection - 2016	Mon 6/6/16	Mon 6/6/16												
LAND USE CONTROL REMEDIAL DESIGN REVISION	Tue 4/1/14	Mon 9/8/14												
Prepare Draft LUCRD Revision	Tue 4/1/14	Fri 6/6/14												
Submit Draft LUCRD	Fri 6/6/14	Fri 6/6/14												
USEPA & MEDEP Review Draft LUCRD Revision	Fri 6/6/14	Wed 8/20/14												
Receive Regulator Comments on Draft LUCRD Revision	Wed 8/13/14	Wed 8/20/14												
Comment Resolution	Wed 8/13/14	Tue 8/26/14												
Prepare Final LUCRD Revision	Wed 8/20/14	Fri 9/5/14												
Submit Final LUCRD Revision	Mon 9/8/14	Mon 9/8/14												



**PORTSMOUTH NAVAL SHIPYARD
SITE MANAGEMENT PLAN SCHEDULE
OPERABLE UNIT 3 (OU3)
(SITE 8, 9 and 11)**

Task Name	Start	Finish	2014				2015				2016					
			Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4		
Second Five Year Evaluation	Sat 10/15/11	Thu 5/31/12														
Operation, Maintenance and Monitoring Plan Implementation	Sat 10/15/11	Thu 5/31/12														
Conduct Eleventh Round	Mon 4/23/12	Thu 9/27/12														
Landfill and LUC Inspection	Mon 6/3/13	Fri 6/3/16	6/3													
Conduct routine inspection, maintenance activities - 2013	Mon 6/3/13	Tue 10/29/13	10/29													
Conduct routine inspection, maintenance activities - 2014	Wed 5/14/14	Thu 5/15/14			5/15											
Conduct routine inspection, maintenance activities - 2015	Mon 6/1/15	Fri 6/5/15								6/5						
Conduct routine inspection, maintenance activities - 2016	Mon 5/30/16	Fri 6/3/16													6/3	
Conduct Environmental Sampling (5-Year Review)	Mon 5/30/16	Fri 6/3/16													6/3	
Gas Monitoring Well Abandonment Plan	Thu 8/22/13	Mon 6/9/14	6/9													
Prepare Draft Gas Well Abandonment Plan	Thu 8/22/13	Tue 10/22/13	10/22													
Submit Draft Gas Well Abandonment Plan	Tue 10/22/13	Tue 10/22/13	10/22													
EPA & MEDEP Review Draft Gas Well Abandonment Plan	Tue 10/22/13	Thu 1/23/14	1/23													
Receive Regulator Comments on Draft Gas Well Abandonment Plan	Wed 11/27/13	Thu 1/23/14	1/23													
Comment Resolution	Thu 1/23/14	Sun 3/9/14		3/9												
Prepare Draft Final Gas Well Abandonment Plan	Sun 3/9/14	Tue 4/22/14			4/22											
Submit Draft Final Gas Well Abandonment Plan	Wed 4/23/14	Wed 4/23/14			4/23											
EPA & MEDEP Review Draft Gas Well Abandonment Plan	Wed 4/23/14	Fri 5/9/14			5/9											
Receive Regulator Comments on Draft Final Gas Well Abandonment Plan	Fri 5/9/14	Fri 5/9/14			5/9											
Prepare Final Gas Well Abandonment Plan	Fri 5/9/14	Mon 6/9/14			6/9											
Submit Final Gas Well Abandonment Plan	Mon 6/9/14	Mon 6/9/14			6/9											
Remedial Action Completion Report	Mon 6/2/14	Fri 5/29/15	5/29													
Prepare Draft RACR	Mon 6/2/14	Fri 10/31/14								10/31						
Submit Draft RACR	Fri 10/31/14	Fri 10/31/14								10/31						
USEPA & MEDEP Review Draft RACR	Fri 10/31/14	Mon 12/15/14								12/15						
Receive Regulator Comments Draft RACR	Mon 12/15/14	Mon 12/15/14								12/15						
Comment Resolution	Mon 12/15/14	Sat 2/28/15									2/28					
Prepare Draft Final RACR	Sat 2/28/15	Mon 3/30/15									3/30					
Submit Draft Final RACR	Mon 3/30/15	Wed 4/29/15									4/29					
USEPA & MEDEP Review Draft Final RACR	Wed 4/29/15	Wed 4/29/15									4/29					
Receive Regulator Comments on Draft Final RACR	Wed 4/29/15	Wed 4/29/15									4/29					
Prepare Final RACR	Wed 4/29/15	Fri 5/29/15										5/29				
Submit Final RACR	Fri 5/29/15	Fri 5/29/15										5/29				



PORTSMOUTH NAVAL SHIPYARD
 SITE MANAGEMENT PLAN SCHEDULE
 OPERABLE UNIT 4 (OU4)
 (SITE 5 and OFFSHORE AOCS)

Task Name	Start	Finish	2014				2015				2016				
			Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	
<u>FEASIBILITY STUDY (FS)</u>	Wed 8/26/09	Mon 9/24/12													
<u>PROPOSED REMEDIAL ACTION PLAN (PRAP)</u>	Wed 6/27/12	Fri 3/29/13													
<u>RECORD OF DECISION (ROD)</u>	Wed 2/13/13	Thu 8/15/13													
Prepare Draft ROD	Wed 2/13/13	Fri 4/26/13													
<i>Submit Draft ROD</i>	Mon 4/29/13	Mon 4/29/13													
USEPA & MEDEP Review Draft ROD	Mon 4/29/13	Thu 5/30/13													
<i>Receive Regulator Comments on Draft ROD</i>	Wed 5/29/13	Thu 5/30/13													
Prepare RTCs & Draft Final ROD	Thu 5/30/13	Mon 7/29/13													
<i>Submit RTCs and Draft Final ROD</i>	Mon 7/29/13	Mon 7/29/13													
MEDEP Submits Letter of Concurrence/Non-Concurrence	Tue 8/6/13	Tue 8/6/13													
USEPA and Navy Sign Final ROD	Wed 8/7/13	Thu 8/15/13													
<u>TIER II SAMPLING AND ANALYSIS PLAN, PRE-REMOVAL SEDIMENT CONFIRMATION SAMPLING</u>	Fri 6/7/13	Mon 9/30/13	9/30												
USEPA & MEDEP Review Draft SAP	Fri 6/7/13	Tue 7/30/13													
<i>Receive Regulator Comments on Draft SAP</i>	Tue 7/9/13	Tue 7/30/13													
Comment Resolution	Wed 7/31/13	Thu 8/22/13													
Prepare Final SAP	Fri 8/23/13	Fri 9/27/13	9/27												
<i>Submit Final SAP</i>	Mon 9/30/13	Mon 9/30/13	9/30												
<u>PRE-REMOVAL CONFIRMATION SEDIMENT SAMPLING</u>	Mon 10/28/13	Tue 9/9/14													
Conduct Pre-Removal Confirmation Sediment Sampling	Mon 10/28/13	Wed 12/11/13													
Prepare and Submit Draft Pre-Removal Confirmation Sediment Sampling Report	Thu 12/12/13	Mon 4/21/14													
USEPA & MEDEP Review Draft Pre-Removal Confirmation Sediment Sampling Report	Mon 4/21/14	Wed 6/11/14													
Comment Resolution	Wed 6/11/14	Mon 8/11/14													
Prepare and Submit Final Pre-Removal Confirmation Sediment Sampling Report	Mon 8/11/14	Tue 9/9/14													
<u>REMEDIAL ACTION</u>	Tue 4/1/14	Mon 2/16/15													
Prepare Remedial Action Workplan	Tue 4/1/14	Tue 9/2/14													
<i>Submit Draft RAWP</i>	Wed 9/3/14	Wed 9/3/14													
USEPA & MEDEP Review Draft RAWP	Wed 9/3/14	Fri 10/3/14													
<i>Receive Regulator Comments on Draft RAWP</i>	Fri 10/3/14	Fri 10/3/14													
Comment Resolution	Fri 10/3/14	Tue 11/18/14													
Prepare Draft Final RAWP	Tue 11/18/14	Wed 12/17/14													



PORTSMOUTH NAVAL SHIPYARD
 SITE MANAGEMENT PLAN SCHEDULE
 OPERABLE UNIT 4 (OU4)
 (SITE 5 and OFFSHORE AOCS)

Task Name	Start	Finish	2014				2015				2016			
			Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4
<i>Submit Draft Final RAWP</i>	Wed 12/17/14	Wed 12/17/14					12/17							
USEPA & MEDEP Review Draft Final RAWP	Wed 12/17/14	Sat 1/17/15					1/17							
<i>Receive Regulator Comments on Draft Final RAWP</i>	Sat 1/17/15	Sat 1/17/15					1/17							
Prepare Final RAWP	Sat 1/17/15	Mon 2/16/15					2/16							
<i>Submit Final RAWP</i>	Mon 2/16/15	Mon 2/16/15					2/16							
CONSTRUCTION	Thu 11/13/14	Thu 4/9/15					4/9							
CONSTRUCTION COMPLETION REPORT	Thu 4/30/15	Mon 1/4/16									1/4			
Prepare Draft CCR	Thu 4/30/15	Wed 7/8/15									7/8			
<i>Submit Draft CCR</i>	Wed 7/8/15	Wed 7/8/15									7/8			
USEPA & MEDEP Review Draft CCR	Wed 7/8/15	Fri 8/21/15									8/21			
<i>Receive Regulator Comments on Draft CCR</i>	Mon 8/24/15	Mon 8/24/15									8/24			
Comment Resolution	Mon 8/24/15	Tue 10/6/15									10/6			
Prepare Draft Final CCR	Tue 10/6/15	Thu 11/5/15									11/5			
<i>Submit Draft Final CCR</i>	Thu 11/5/15	Thu 11/5/15									11/5			
USEPA & MEDEP Review Draft Final CCR	Thu 11/5/15	Sat 12/5/15									12/5			
<i>Receive Regulator Comments on Draft Final CCR</i>	Sat 12/5/15	Sat 12/5/15									12/5			
Prepare Final CCR	Sat 12/5/15	Mon 1/4/16									1/4			
<i>Submit Final CCR</i>	Mon 1/4/16	Mon 1/4/16									1/4			



PORTSMOUTH NAVAL SHIPYARD
 SITE MANAGEMENT PLAN SCHEDULE
 OPERABLE UNIT 7 (OU7)
 (SITE 32)

Task Name	Start	Finish	2014				2015				2016			
			Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
FEASIBILITY STUDY (FS)	Fri 5/18/12	Thu 6/13/13												
PROPOSED REMEDIAL ACTION PLAN (PRAP)	Wed 3/27/13	Wed 8/14/13												
Prepare Draft PRAP	Wed 3/27/13	Thu 5/23/13												
<i>Submit Draft PRAP</i>	Fri 5/24/13	Fri 5/24/13												
USEPA & MEDEP Review Draft PRAP	Fri 5/24/13	Fri 6/21/13												
<i>Receive Regulator Comments on Draft PRAP</i>	Thu 6/20/13	Fri 6/21/13												
Prepare RTCs & Final PRAP	Mon 6/24/13	Fri 7/12/13												
<i>Submit Final PRAP</i>	Fri 7/12/13	Fri 7/12/13												
Public Comment Period	Tue 7/16/13	Wed 8/14/13												
RECORD OF DECISION	Mon 6/3/13	Mon 9/30/13	9/30											
Prepare Draft ROD	Mon 6/3/13	Tue 7/23/13												
<i>Submit Draft ROD</i>	Wed 7/24/13	Wed 7/24/13												
USEPA & MEDEP Review Draft ROD	Thu 7/25/13	Tue 8/27/13												
<i>Receive Regulator Comments on Draft ROD</i>	Wed 8/21/13	Tue 8/27/13												
Prepare RTCs & Final ROD	Fri 8/23/13	Thu 9/12/13	12											
<i>Submit Final ROD for Signature</i>	Fri 9/13/13	Fri 9/13/13	9/13											
MEDEP Submits Letter of Concurrence/Non-Concurrence	Wed 9/18/13	Wed 9/18/13	9/18											
USEPA and Navy Sign Final ROD	Fri 9/27/13	Mon 9/30/13	9/30											
LAND USE CONTROL REMEDIAL DESIGN	Thu 10/3/13	Wed 10/29/14												
Prepare Draft LUCRD	Thu 10/3/13	Mon 12/23/13												
<i>Submit Draft LUCRD</i>	Tue 12/24/13	Tue 12/24/13												
USEPA & MEDEP Review Draft LUCRD	Tue 12/24/13	Tue 2/25/14												
<i>Receive Regulator Comments on Draft LUCRD</i>	Thu 2/6/14	Tue 2/25/14												
Comment Resolution	Tue 2/25/14	Wed 7/30/14												
Prepare Draft Final LUCRD	Wed 7/30/14	Fri 8/29/14												
<i>Submit Draft Final LUCRD</i>	Fri 8/29/14	Fri 8/29/14												
USEPA & MEDEP Review Draft Final LUCRD	Fri 8/29/14	Sun 9/28/14												
<i>Receive Regulator Comments on Draft Final LUCRD</i>	Mon 9/29/14	Mon 9/29/14												
Prepare Final LUCRD	Mon 9/29/14	Wed 10/29/14												
<i>Submit Final LUCRD</i>	Wed 10/29/14	Wed 10/29/14												
REMEDIAL ACTION	Thu 5/1/14	Wed 1/21/15												
Prepare Remedial Action Work Plan	Thu 5/1/14	Thu 7/24/14												
<i>Submit Draft RAWP</i>	Thu 7/24/14	Thu 7/24/14												



PORTSMOUTH NAVAL SHIPYARD
 SITE MANAGEMENT PLAN SCHEDULE
 OPERABLE UNIT 7 (OU7)
 (SITE 32)

Task Name	Start	Finish	2014				2015				2016			
			Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
USEPA & MEDEP Review Draft RAWP	Thu 7/24/14	Mon 9/8/14				9/8								
<i>Receive Regulator Comments on Draft RAWP</i>	Mon 9/8/14	Mon 9/8/14				9/8								
Comment Resolution	Mon 9/8/14	Thu 10/23/14				10/23								
Prepare Draft Final RAWP	Thu 10/23/14	Fri 11/21/14				11/21								
<i>Submit Draft Final RAWP</i>	Fri 11/21/14	Fri 11/21/14				11/21								
USEPA & MEDEP Review Draft Final RAWP	Fri 11/21/14	Mon 12/22/14				12/22								
<i>Receive Regulator Comments on Draft Final RAWP</i>	Mon 12/22/14	Mon 12/22/14				12/22								
Prepare Final RAWP	Mon 12/22/14	Wed 1/21/15				1/21								
<i>Submit Final RAWP</i>	Wed 1/21/15	Wed 1/21/15				1/21								
CONSTRUCTION	Mon 12/1/14	Thu 4/30/15							4/30					
CONSTRUCTION COMPLETION REPORT	Thu 4/30/15	Thu 1/7/16											1/7	
Prepare Draft CCR	Thu 4/30/15	Fri 7/10/15							7/10					
<i>Submit Draft CCR</i>	Fri 7/10/15	Fri 7/10/15							7/10					
USEPA & MEDEP Review Draft CCR	Fri 7/10/15	Mon 8/24/15												
<i>Receive Regulator Comments on Draft CCR</i>	Mon 8/24/15	Mon 8/24/15												
Comment Resolution	Mon 8/24/15	Thu 10/8/15												
Prepare Draft Final CCR	Thu 10/8/15	Fri 11/6/15												
<i>Submit Draft Final CCR</i>	Fri 11/6/15	Fri 11/6/15												
USEPA & MEDEP Review Draft Final CCR	Fri 11/6/15	Mon 12/7/15												
<i>Receive Regulator Comments on Draft Final CCR</i>	Mon 12/7/15	Mon 12/7/15												
Prepare Final CCR	Mon 12/7/15	Thu 1/7/16												
<i>Submit Final CCR</i>	Thu 1/7/16	Thu 1/7/16												
LUC INSPECTIONS	Wed 6/3/15	Fri 6/10/16												6/10
Conduct LUC Inspection - 2015	Wed 6/3/15	Sun 6/7/15							6/7					
Conduct LUC Inspection - 2016	Mon 6/6/16	Fri 6/10/16												6/10



PORTSMOUTH NAVAL SHIPYARD
 SITE MANAGEMENT PLAN SCHEDULE
 OPERABLE UNIT 8 (OU8)
 (SITE 31)

Task Name	Start	Finish	2014				2015				2016			
			Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4
REMEDIAL INVESTIGATION SAMPLING AND ANALYSIS PLAN (SAP)	Wed 1/15/14	Fri 11/28/14		[Task Bar]				11/28						
Prepare Draft Sampling and Analysis Plan	Wed 1/15/14	Wed 4/30/14		[Task Bar]		4/30								
<i>Submit Draft SAP</i>	Wed 4/30/14	Wed 4/30/14			4/30									
USEPA & MEDEP Review Draft SAP	Wed 4/30/14	Fri 6/13/14			[Task Bar]		6/13							
<i>Receive Regulatory Comments on Draft SAP</i>	Mon 6/16/14	Mon 6/16/14			6/16									
Comment Resolution	Mon 6/16/14	Sat 8/30/14			[Task Bar]		8/30							
Prepare Draft Final SAP	Sat 8/30/14	Mon 9/29/14			[Task Bar]		9/29							
<i>Submit Draft Final SAP</i>	Mon 9/29/14	Mon 9/29/14				9/29								
USEPA & MEDEP Review Draft Final SAP	Mon 9/29/14	Wed 10/29/14			[Task Bar]		10/29							
<i>Receive Regulatory Comments on Draft Final SAP</i>	Wed 10/29/14	Wed 10/29/14				10/29								
Prepare Final SAP	Wed 10/29/14	Fri 11/28/14			[Task Bar]		11/28							
<i>Submit Final SAP</i>	Fri 11/28/14	Fri 11/28/14				11/28								
RI FIELD WORK AND DATA MANAGEMENT	Mon 12/15/14	Mon 3/30/15			[Task Bar]				3/30					
REMEDIAL INVESTIGATION (RI)	Fri 4/3/15	Wed 3/30/16			[Task Bar]				3/30					
Prepare Draft RI	Fri 4/3/15	Mon 8/31/15			[Task Bar]				8/31					
<i>Submit Draft RI</i>	Mon 8/31/15	Mon 8/31/15				8/31								
USEPA & MEDEP Review Draft RI	Mon 8/31/15	Thu 10/15/15			[Task Bar]		10/15							
<i>Receive Regulatory Comments on Draft RI</i>	Thu 10/15/15	Thu 10/15/15				10/15								
Comment Resolution	Thu 10/15/15	Tue 12/29/15			[Task Bar]		12/29							
Prepare Draft Final RI	Tue 12/29/15	Thu 1/28/16			[Task Bar]		1/28							
<i>Submit Draft Final RI</i>	Thu 1/28/16	Thu 1/28/16				1/28								
USEPA & MEDEP Review Draft Final RI	Fri 1/29/16	Mon 2/29/16			[Task Bar]		2/29							
<i>Receive Regulatory Comments on Draft Final RI</i>	Tue 3/1/16	Tue 3/1/16				3/1								
Prepare Final RI	Tue 3/1/16	Wed 3/30/16			[Task Bar]		3/30							
<i>Submit Final RI</i>	Wed 3/30/16	Wed 3/30/16				3/30								
FEASIBILITY STUDY	Tue 3/29/16	Fri 1/27/17			[Task Bar]									
Prepare Draft FS	Tue 3/29/16	Tue 6/28/16			[Task Bar]				6/28					
<i>Submit Draft FS</i>	Tue 6/28/16	Tue 6/28/16				6/28								
USEPA & MEDEP Review Draft FS	Tue 6/28/16	Fri 8/12/16			[Task Bar]		8/12							
<i>Receive Regulatory Comments on Draft FS</i>	Fri 8/12/16	Fri 8/12/16				8/12								
Comment Resolution	Mon 8/15/16	Fri 10/28/16			[Task Bar]									
Prepare Draft Final FS	Mon 10/31/16	Mon 11/28/16			[Task Bar]									



PORTSMOUTH NAVAL SHIPYARD
 SITE MANAGEMENT PLAN SCHEDULE
 OPERABLE UNIT 8 (OU8)
 (SITE 31)

Task Name	Start	Finish	2014				2015				2016			
			Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4
<i>Submit Draft Final FS</i>	Mon 11/28/16	Mon 11/28/16												
USEPA & MEDEP Review Draft Final FS	Mon 11/28/16	Wed 12/28/16												
<i>Receive Regulatory Comments on Draft Final FS</i>	Wed 12/28/16	Wed 12/28/16												
Prepare Final FS	Wed 12/28/16	Fri 1/27/17												
<i>Submit Final FS</i>	Fri 1/27/17	Fri 1/27/17												
PRAP	Tue 12/13/16	Fri 5/5/17												
RECORD OF DECISION	Thu 3/30/17	Thu 9/21/17												



PORTSMOUTH NAVAL SHIPYARD
 SITE MANAGEMENT PLAN SCHEDULE
 OPERABLE UNIT 9 (OU9)
 (SITE 34)

Task Name	Start	Finish	2014				2015				2016			
			Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
FEASIBILITY STUDY (FS)	Fri 6/22/12	Fri 5/31/13												
PROPOSED REMEDIAL ACTION PLAN	Fri 3/15/13	Wed 8/14/13												
Prepare Draft PRAP	Fri 3/15/13	Fri 5/31/13												
<i>Submit Draft PRAP</i>	Fri 5/31/13	Fri 5/31/13												
USEPA & MEDEP Review Draft PRAP	Fri 5/31/13	Tue 6/25/13												
<i>Receive Regulator Comments on DRAFT PRAP</i>	Thu 6/20/13	Tue 6/25/13												
Prepare Draft Final PRAP & RTCs	Wed 6/26/13	Fri 7/12/13												
<i>Submit Draft Final PRAP and RTCs</i>	Fri 7/12/13	Fri 7/12/13												
Public Comment Period	Tue 7/16/13	Wed 8/14/13												
RECORD OF DECISION (ROD)	Tue 6/4/13	Mon 9/30/13	9/30											
Prepare Draft ROD	Tue 6/4/13	Mon 7/29/13												
<i>Submit Draft ROD</i>	Mon 7/29/13	Mon 7/29/13												
USEPA & MEDEP Review Draft ROD	Mon 7/29/13	Thu 8/29/13												
<i>Receive Regulator Comments on Draft ROD</i>	Wed 8/21/13	Thu 8/29/13												
Prepare RTCs & Final ROD	Fri 8/23/13	Thu 9/12/13	12											
<i>Submit RTCs and Final ROD</i>	Fri 9/13/13	Fri 9/13/13	13											
MEDEP Submits Letter of Concurrence/Non-Concurrence	Wed 9/18/13	Wed 9/18/13	9/18											
USEPA & Navy Sign Final ROD	Fri 9/27/13	Mon 9/30/13	9/30											
LAND USE CONTROL REMEDIAL DESIGN	Thu 10/3/13	Mon 10/6/14	10/6											
Prepare Draft LUCRD	Thu 10/3/13	Mon 12/23/13	12/23											
<i>Submit Draft LUCRD</i>	Tue 12/24/13	Tue 12/24/13	12/24											
USEPA & MEDEP Review Draft LUCRD	Tue 12/24/13	Tue 2/25/14	2/25											
<i>Receive Regulator Comments on Draft LUCRD</i>	Thu 2/6/14	Tue 2/25/14	2/25											
Comment Resolution	Tue 2/25/14	Mon 7/7/14	7/7											
Prepare Draft Final LUCRD	Mon 7/7/14	Wed 8/6/14	8/6											
<i>Submit Draft LUCRD</i>	Wed 8/6/14	Wed 8/6/14	8/6											
USEPA & MEDEP Review Draft Final LUCRD	Wed 8/6/14	Fri 9/5/14	9/5											
<i>Receive Regulator Comments on Draft Final LUCRD</i>	Fri 9/5/14	Fri 9/5/14	9/5											
Prepare Final LUCRD	Fri 9/5/14	Sun 10/5/14	10/5											
<i>Submit Final LUCRD</i>	Mon 10/6/14	Mon 10/6/14	10/6											
REMEDIAL ACTION CLOSEOUT REPORT	Tue 4/1/14	Wed 4/29/15	4/29											
Prepare Draft RACR	Tue 4/1/14	Tue 9/30/14	9/30											
<i>Submit Draft RACR</i>	Tue 9/30/14	Tue 9/30/14	9/30											
USEPA & MEDEP Review Draft RACR	Tue 9/30/14	Fri 11/14/14	11/14											
<i>Receive Regulator Comments on Draft RACR</i>	Fri 11/14/14	Fri 11/14/14	11/14											
Comment Resolution	Fri 11/14/14	Wed 1/28/15	1/28											



PORTSMOUTH NAVAL SHIPYARD
 SITE MANAGEMENT PLAN SCHEDULE
 OPERABLE UNIT 9 (OU9)
 (SITE 34)

Task Name	Start	Finish	2014				2015				2016			
			Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Prepare Draft Final RACR	Wed 1/28/15	Fri 2/27/15						2/27						
<i>Submit Draft Final RACR</i>	Fri 2/27/15	Fri 2/27/15						2/27						
USEPA & MEDEP Review Draft Final RACR	Fri 2/27/15	Mon 3/30/15							3/30					
<i>Receive Regulator Comments on Draft Final RACR</i>	Mon 3/30/15	Mon 3/30/15							3/30					
Prepare Final RACR	Mon 3/30/15	Wed 4/29/15								4/29				
<i>Submit Final RACR</i>	Wed 4/29/15	Wed 4/29/15								4/29				
LUC INSPECTIONS	Mon 6/1/15	Fri 6/10/16												6/10
Conduct LUC Inspection - 2015	Mon 6/1/15	Fri 6/5/15								6/5				
Conduct LUC Inspection - 2016	Mon 6/6/16	Fri 6/10/16												6/10



PORTSMOUTH NAVAL SHIPYARD
SITE MANAGEMENT PLAN SCHEDULE
SITE 30

Task Name	Start	Finish	2014				2015				2016			
			Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4
CONSTRUCTION COMPLETION REPORT (CCR)	Mon 11/21/11	Wed 11/27/13	█ 11/27											
Prepare CCR	Mon 11/21/11	Tue 6/11/13												
Submit Draft CCR	Wed 6/12/13	Wed 6/12/13												
USEPA & MEDEP Review Draft CCR	Wed 6/12/13	Tue 7/30/13												
Receive Regulator Comments on Draft CCR	Tue 7/30/13	Tue 7/30/13												
Comment Resolution	Wed 7/31/13	Tue 11/12/13	█ 11/12											
Prepare Final CCR	Wed 11/13/13	Wed 11/27/13	█ 11/27											
Submit Final CCR	Wed 11/27/13	Wed 11/27/13	█ 11/27											
DECISION DOCUMENT	Fri 3/1/13	Tue 4/15/14	█ 4/15											
Prepare Decision Document	Fri 3/1/13	Wed 5/15/13												
Submit Draft Decision Document	Thu 5/16/13	Thu 5/16/13												
USEPA & MEDEP Review Draft Decision Document	Thu 5/16/13	Thu 7/25/13												
Receive Regulator Comments on Draft Decision Document	Wed 7/3/13	Thu 7/25/13												
Comment Resolution	Thu 7/25/13	Wed 10/16/13	█ 10/16											
Prepare Draft Final Decision Document	Wed 10/16/13	Fri 12/20/13	█ 12/20											
Submit Draft Final Decision Document	Mon 12/23/13	Mon 12/23/13	█ 12/23											
Public Comment Period	Tue 1/7/14	Thu 2/6/14	█ 2/6											
Prepare Final Decision Document	Fri 2/7/14	Thu 2/13/14	█ 2/13											
Navy Signs Final Decision Document	Thu 3/6/14	Thu 3/6/14	█ 3/6											
Submit Final Decision Document	Thu 3/13/14	Thu 3/13/14	█ 3/13											
EPA and MEDEP Submits Letter of Concurrence	Mon 3/17/14	Tue 4/15/14	█ 4/15											



Attachment C

Schedule Revisions For FY15 Amended Site Management Plan

Schedule Revisions For
FY15 Amended Site Management Plan
Environmental Restoration Program
Portsmouth Naval Shipyard, Kittery, Maine

Schedule revisions for each Operable Unit (OU) shown in the Appendix B reflect schedule changes to the Final Fiscal Year 2014 (FY14) Amended Site Management Plan (SMP) based on the status of projects as of September 1, 2014.

OU1 (Site 10)

- The Groundwater Monitoring Report and Construction Completion Report dates were updated to reflect actual submittal of the final documents in July and September 2013, respectively, both ahead of schedule.

OU2 (Sites 6 and 29)

- Submittal of draft Construction Completion Reports for WDA and DRMO Area were delayed approximately two months from July to September 2014 to account for the actual end of Remedial Action construction in Summer 2014. Completion of construction was extended to allow for appropriate disposal of excavated characterized as hazardous and approval of the on-site soil treatment method to enable off-site disposal of excavated soil as a non-hazardous waste.

OU3 (Sites 8, 9, and 11)

- The schedule for the Remedial Action Completion Report has been updated to reflect submittal of the draft report in June 2014, four months ahead of schedule from the Final FY14 SMP.

OU4 (Site 5 and offshore areas potentially impacted by onshore sites)

- The draft sediment sampling data report was submitted approximately two months later than anticipated in the FY14 SMP, corresponding to the sediment sampling event being completed approximately three months later than anticipated in the FY 14 SMP.
- Remedial Action Work Plan (RAWP) dates were updated to reflect review of the pre-removal sediment sampling and preparation of Navy's internal remedial design. Consistent with the approved Schedule Extension Request, the draft RAWP will be submitted in September 2014 compared with an anticipated date of February 2014 in

the FY 2014 SMP. The anticipated start time for Remedial Action in Fall 2014 has not been impacted.

OU7 (Site 32)

- The schedule for the Land Use Control Remedial Design (LUCRD) was updated to reflect the approved Schedule Extension Request to allow the Navy to resolve regulatory and Navy concerns identified during update to the LUC RD for OU1 before responding to regulatory comments on the draft LUC RD for OU7. The final LUCRD will be submitted in September 2014 compared with the anticipated date of July 2014 in the FY 2014 SMP.
- The schedule for the Remedial Action Work Plan for OU7 has been updated to reflect the submitted Schedule Extension Request for submittal of the draft plan in Summer 2014. The anticipated start time for Remedial Action in December 2014 has not been impacted.

OU8 (Site 31)

- The schedule for the OU8 Remedial Investigation (RI) has been updated due to the delays in preparation of the Sampling and Analysis Plan (SAP). Remedial Investigation field activities will commence within one month of submittal of the final SAP.

OU9 (Site 34)

- The schedule for the LUCRD was updated to reflect the approved Schedule Extension Request to allow the Navy to resolve regulatory and Navy concerns identified during update to the LUC RD for OU1 before responding to regulatory comments on the draft LUC RD for OU9. The final LUCRD will be submitted in September 2014 compared with the anticipated date of July 2014 in the FY 2014 SMP.

Site 30

- The Construction Completion Report and Decision Document schedules were updated to reflect actual submittal of the final documents in November 2013 and March 2014, respectively.
